

December 10, 2025

Federal Energy Regulatory Commission 888 First Street, N.E. Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Secretary

Re: Colorado Interstate Gas Company, L.L.C.

Docket No. CP24-124-000

Monthly Status Report No. 7

Commissioners:

Colorado Interstate Gas Company, L.L.C. ("CIG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP24-124-000, its monthly status report related to the Totem Enhanced Delivery Project ("Project").

Description of Proceeding

On April 8, 2024, CIG submitted an application pursuant to sections 7(b) and 7(c) of the Natural Gas Act¹ and Part 157 of the Commission's regulations² for authorizations to: (1) increase the maximum withdrawal rate by approximately 50 million cubic feet per day; (2) install six new injection and withdrawal wells; (3) replace and install various sections of storage pipeline; (4) reclassify one existing injection/withdrawal well to an observation well; (5) install various appurtenant and auxiliary facilities; and (6) inject approximately one billion cubic feet of additional base gas into the Totem storage field. On March 20, 2025, the Commission issued an Order granting CIG's requested authorizations.³ Subsequently, on May 14, 2025, the Commission approved CIG's Implementation Plan filed on May 7, 2025 and issued CIG a partial notice to proceed with construction of the storage wells and pipeline related work of the Project. Thereafter on July 23, 2025, the Commission issued CIG its full notice to proceed related to Project construction.

Submittal of Status Report

In compliance with Environmental Condition No. 8 of Appendix B to the Order, CIG is herewith filing their Monthly Status Report No. 7 for the period of November 1, 2025 through November 30, 2025.

¹ 15 U.S.C. § 717(f)(b)-(c).

² 18 C.F.R. §§ 157.1 – 157.218 (2025) (Part 157).

³ See Colorado Interstate Gas Company, L.L.C., 190 FERC ¶ 62,174 (2025).

Filing Information

CIG is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet,* guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

Respectfully submitted, COLORADO INTERSTATE GAS COMPANY, L.L.C.

By /s/ Francisco Tarín
Francisco Tarín
Director, Regulatory

Enclosures

Cc. Ms. Olubukola Pope, OEP Ms. Sydney Harris, OEP

CIG's Monthly Status Report No. 7		
Docket No. CP24-124-000		
Project Name:	Totem Enhanced Deliverability Project	
County/State:	Adams County, Colorado	Date: 12/10/2025
Reporting Period:	November 1, 2025 – November 30, 2025	
Environmental Inspector:	Sam Sears	

1. UPDATE ON EFFORTS TO OBTAIN NECESSARY FEDERAL AUTHORIZATIONS:

CIG has received all necessary federal authorizations required for the Project.

2. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:

Injection/Withdrawal Wells

During this reporting period, CIG's contractor completed drilling activities on Injection/Withdrawal ("I/W") Well Nos. 29 and 30. Production tubing was successfully installed on I/W Well Nos. 26, 25, and 29. In addition, reclamation efforts continued across previously disturbed pad sites to restore them to pre-construction conditions.

Storage Pipeline Laterals

At the I/W Well No. 28 well pad, CIG's contractor constructed the concrete foundations and installed associated piping, including lateral connections, drain lines, and fuel gas piping. At the I/W Well No. 27 well pad, CIG's contractor constructed concrete foundations and piping systems. Additionally, concrete foundation work was completed at the I/W Well No. 25 well pad in preparation for facility installation.

Compressor Station

During this reporting period, backfilling was completed at the new Lateral 254F-1 receiver. In addition, hydrostatic testing was performed on the drain piping connected to the V-5530A horizontal vessel.

3. RELEVANT ENVIRONMENTAL ACTIVITIES:

During this reporting period, the Environmental Inspector (EI) and CIG personnel provided environmental training to seven (7) project personnel.

4. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN:

No environmental problems or issues occurred during this reporting period.

5. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS:

No environmental compliance issues or resolutions occurred during this reporting period.

6. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS:

No environmental compliance issues or resolutions occurred during this reporting period.

7. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD:

Injection/Withdrawal Wells

CIG anticipates completing the installation of production tubing for I/W Well No. 30 during the next reporting period. In addition, the contractor will continue restoration and reclamation activities on the completed well pads and remaining disturbed sites to restore them to pre-construction conditions. Finally, flowback operations are scheduled to begin on multiple wells to initiate production testing and system integrity verification.

Storage Pipeline Laterals

CIG anticipates continuing construction and installation activities at the I/W Nos. 25, 26, 27, 28, and 29 well pads during the next reporting period. Activities to be conducted at these well pads will include piping

installation, building construction, electrical and instrumentation systems, site improvements, along with installation of the lateral, drain line, and fuel gas piping, and concrete foundation installation.
<u>Compressor Station</u> At the compressor station, CIG anticipates completion of backfill activities at the new receiver in the compressor station yard, as well as installing piping to the horizontal vessel and installing instrumentation for the new vertical scrubber and horizontal vessel.

Project: Totem Enhanced Delivery Project

Direction of Photo:

Southeast

Date: November 3,

2025

Description: Erosion control devices installed on the perimeter of I/W Well

No. 27.



Project: Totem Enhanced Delivery Project

Direction of Photo:

West

Date: November 4,

2025

Description: Diversion ditch between pad and topsoil with rock check dams at I/W Well No. 27.



Project: Totem Enhanced Delivery

Project

Direction of Photo:

North

Date: November 5,

2025

Description: Silt fence on east side of Lateral

254 ROW.



Location: Totem Enhanced Delivery

Project

Direction of Photo:

North

Date: November 8,

2025

Description: Paint

booth.



Project: Totem Enhanced Delivery

Project

Direction of Photo:

East

Date: November 11,

2025

Description:

Excavated trench at the I/W Well No. 28 well pad with topsoil segregation and silt fence in preparation for installation of piping and lateral connections.



Project: Totem Enhanced Delivery Project

Direction of Photo:

North

Date: November 13

2025

Description: Drill rig being set up on the I/W Well No. 30 well

pad.



Project: Totem Enhanced Delivery Project

Direction of Photo:

South

Date: November 17,

2025

Description: Restored pre-construction contours and replaced topsoil at the I/W Well No. 27 well pad.



Project: Totem Enhanced Delivery Project

Direction of Photo:


North

Date: November 18,

2025

Description:

Completed concrete forms at the I/W Well No. 27 well pad.

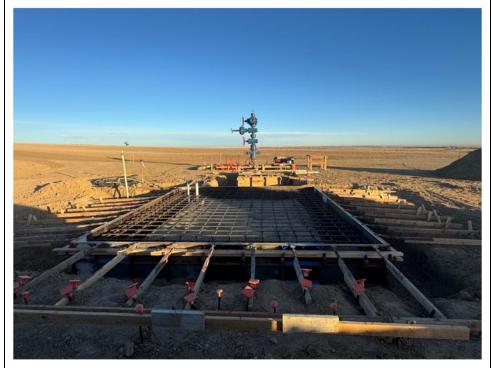

Project: Totem Enhanced Delivery

Project

Direction of Photo:

West

Date: November 19,

2025

Description: Water truck completing dust

control.



Project: Totem Enhanced Delivery

Project

Direction of Photo:

South

Date: November 22,

2025


Description: View of the eastern edge of the I/W Well No. 27 well pad back to original contours; topsoil has been replaced.



Certificate of Service

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 10th day of December 2025.



Two North Nevada Avenue Colorado Springs, Colorado 80903 (719) 667-7517
