



February 24, 2026

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Secretary

Re: Colorado Interstate Gas Company, L.L.C.
Docket No. CP24-124-000
Monthly Status Report No. 9

Commissioners:

Colorado Interstate Gas Company, L.L.C. (“CIG”) is hereby filing with the Federal Energy Regulatory Commission (“Commission”) in Docket No. CP24-124-000, its monthly status report related to the Totem Enhanced Delivery Project (“Project”).

Description of Proceeding

On April 8, 2024, CIG submitted an application pursuant to sections 7(b) and 7(c) of the Natural Gas Act¹ and Part 157 of the Commission’s regulations² for authorizations to: (1) increase the maximum withdrawal rate by approximately 50 million cubic feet per day; (2) install six new injection and withdrawal wells; (3) replace and install various sections of storage pipeline; (4) reclassify one existing injection/withdrawal well to an observation well; (5) install various appurtenant and auxiliary facilities; and (6) inject approximately one billion cubic feet of additional base gas into the Totem storage field. On March 20, 2025, the Commission issued an Order granting CIG’s requested authorizations.³ Subsequently, on May 14, 2025, the Commission approved CIG’s Implementation Plan filed on May 7, 2025 and issued CIG a partial notice to proceed with construction of the storage wells and pipeline related work of the Project. Thereafter on July 23, 2025, the Commission issued CIG its full notice to proceed related to Project construction.

Submittal of Status Report

In compliance with Environmental Condition No. 8 of Appendix B to the Order, CIG is herewith filing their Monthly Status Report No. 9 for the period of January 1, 2026 through January 31, 2026.

¹ 15 U.S.C. § 717(f)(b)-(c).

² 18 C.F.R. §§ 157.1 – 157.218 (2025) (Part 157).

³ See *Colorado Interstate Gas Company, L.L.C.*, 190 FERC ¶ 62,174 (2025).

Filing Information

CIG is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

Respectfully submitted,
COLORADO INTERSTATE GAS
COMPANY, L.L.C.

By /s/ Francisco Tarín
Francisco Tarín
Director, Regulatory

Enclosures

Cc. Ms. Olubukola Pope, OEP
Ms. Sydney Harris, OEP

Colorado Interstate Gas Company, L.L.C. (CIG)

CIG's Monthly Status Report No. 9		
Docket No. CP24-124-000		
Project Name:	Totem Enhanced Deliverability Project	
County/State:	Adams County, Colorado	Date: 2/24/2026
Reporting Period:	January 1, 2026 – January 31, 2026	
Environmental Inspector:	Sam Sears	
<p>1. UPDATE ON EFFORTS TO OBTAIN NECESSARY FEDERAL AUTHORIZATIONS: CIG has received all necessary federal authorizations required for the Project. On January 28, 2026, FERC authorized CIG's request to place its Project facilities into service. CIG continues to work through final commissioning and testing activities that are necessary to place its Project into service.</p> <p>2. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</p> <p><u>Injection/Withdrawal Wells</u> During this reporting period, CIG's contractor completed clean out and back flow activities at Injection/Withdrawal ("I/W") Well Nos. 29 and 30. In addition, all well site restoration was completed.</p> <p><u>Storage Pipeline Laterals</u> During this reporting period, CIG's contractor focused on completing well facility and lateral work, tie-in of well lateral lines to Line 254F-1, electrical and instrumentation installation and fencing activities at I/W Well Nos. 25, 26, 27, 28, and 29. Well facility and lateral work including tie-in of the well lateral line to the 254F-2 mainline was completed at I/W Well No. 30. In addition, the well pad building at I/W Well No. 30 was completed.</p> <p><u>Compressor Station</u> During this reporting period, the heat trace and insulation was installed on the vertical and horizontal heat scrubbers. In addition, electrical and instrumentation equipment to support the new vertical scrubber and horizontal vessel was completed.</p> <p>3. RELEVANT ENVIRONMENTAL ACTIVITIES: No new personnel were on site during this reporting period therefore no applicable environmental training was conducted.</p> <p>4. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN: No environmental problems or issues occurred during this reporting period.</p> <p>5. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS: No environmental compliance issues occurred during this reporting period.</p> <p>6. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS: No landowner issues or concerns were identified during this reporting period.</p> <p>7. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD: During the next reporting period, CIG will continue final commissioning and testing activities. CIG anticipates completing well facility and lateral backfill and restoration work, completing restoration of all temporary roads, and completing station programming on the new equipment at the compressor station.</p>		

Colorado Interstate Gas Company, L.L.C. (CIG)

Project: Totem Enhanced Delivery Project
Direction of Photo: East
Date: January 2, 2026
Description: Restored topsoil along Line 254-F1 with permanent silt fence still in place.



Project: Totem Enhanced Delivery Project
Direction of Photo: Southwest
Date: January 3, 2026
Description: Contractor installing fencing at I/W Well No. 27.



Colorado Interstate Gas Company, L.L.C. (CIG)

Project: Totem Enhanced Delivery Project
Direction of Photo: Northeast
Date: January 9, 2026
Description: Contractor installing pre-fabricated building at I/W Well No. 29.



Location: Totem Enhanced Delivery Project
Direction of Photo: Southeast
Date: January 17, 2026
Description: Replacing topsoil on the lateral ROW at I/W Well No. 29.



Colorado Interstate Gas Company, L.L.C. (CIG)

Project: Totem Enhanced Delivery Project

Direction of Photo: East

Date: January 12, 2026

Description: Excavated trench for the lateral connecting I/W Well No. 30.



Project: Totem Enhanced Delivery Project

Direction of Photo: East

Date: January 11, 2026

Description: I/W Well No. 25 with topsoil restored.



Colorado Interstate Gas Company, L.L.C. (CIG)

Project: Totem Enhanced Delivery Project
Direction of Photo: North
Date: January 23, 2026
Description: Restored Lateral ROW at I/W Well No. 25.




Project: Totem Enhanced Delivery Project
Direction of Photo: South
Date: January 22, 2026
Description: Contractor backfilling around one of the emergency shutoff panels.



Colorado Interstate Gas Company, L.L.C. (CIG)

Project: Totem Enhanced Delivery Project
Direction of Photo: East
Date: January 21, 2026
Description: Completed lateral piping connecting I/W Well No. 28.

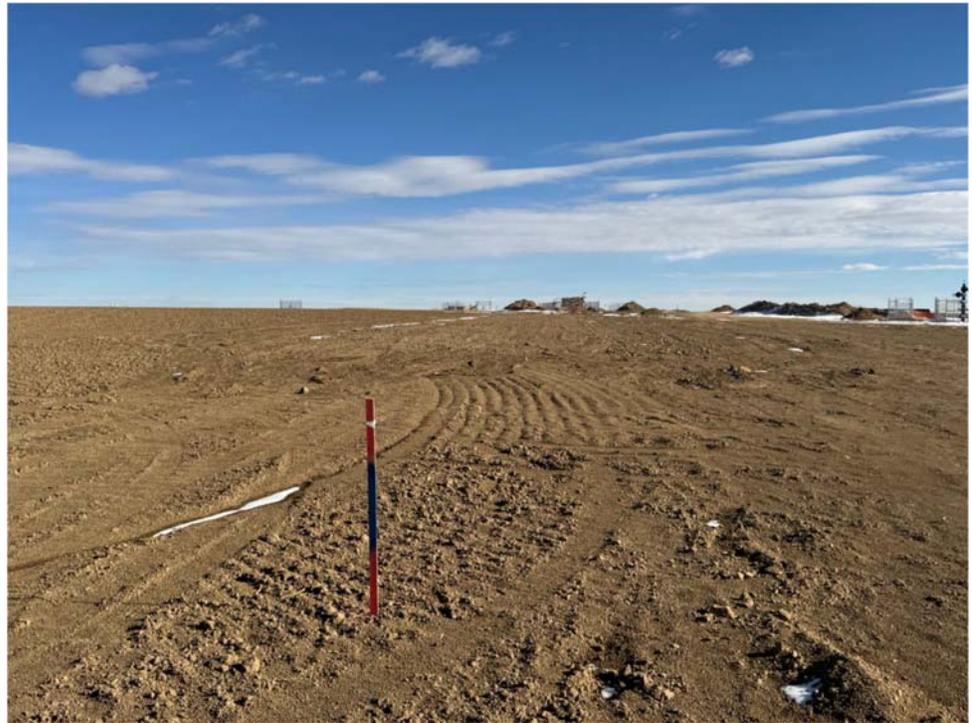

Project: Totem Enhanced Delivery Project
Direction of Photo: Northeast
Date: January 31, 2026
Description: I/W Well No. 25 and access road.



Certificate of Service

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 24th day of February 2026.

/s/

Francisco Tarín

Two North Nevada Avenue
Colorado Springs, Colorado 80903
(719) 667-7517
