



El Paso Natural Gas
Company, L.L.C.
a Kinder Morgan company

August 7, 2026

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Secretary

Re: El Paso Natural Gas Company, L.L.C.;
Docket No. CP24-520-000
Maricopa Lateral Expansion Project
Weekly Environmental Inspector Report No. 35

Commissioners:

El Paso Natural Gas Company, L.L.C. ("EPNG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP24-520-000, its weekly construction status report related to EPNG's Maricopa Lateral Expansion Project ("Project").

Description of Proceeding

On September 17, 2024, EPNG filed a prior notice request, pursuant to Section 7 of the Natural Gas Act ("NGA") and Sections 157.205, 157.208 and 157.210 of the Commission's Part 157 blanket certificate regulations, seeking authorization to construct, install and operate the new Haystack Compressor Station and appurtenances to be located in Yavapai County, Arizona.¹ The Project is designed to provide an additional 50,517 dekatherms per day of firm transportation service to Maricopa County, Arizona.

Submittal of Status Report

In compliance with Section 157.208(c)(10) of the NGA, EPNG is providing its Environmental Inspector Report No. 35.

¹ On October 1, 2024, the Commission issued a Notice of Request Under Blanket Authorization initiating the 60-day comment period. Protests to the Project were timely filed and not withdrawn during the reconciliation period. On July 24, 2025, the Commission issued an Order Denying Protest and Authorizing Construction under EPNG's blanket certificate. See *El Paso Natural Gas Company, L.L.C.*, 192 FERC ¶ 61,078 (2025).

Filing Information

EPNG is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

Respectfully submitted,

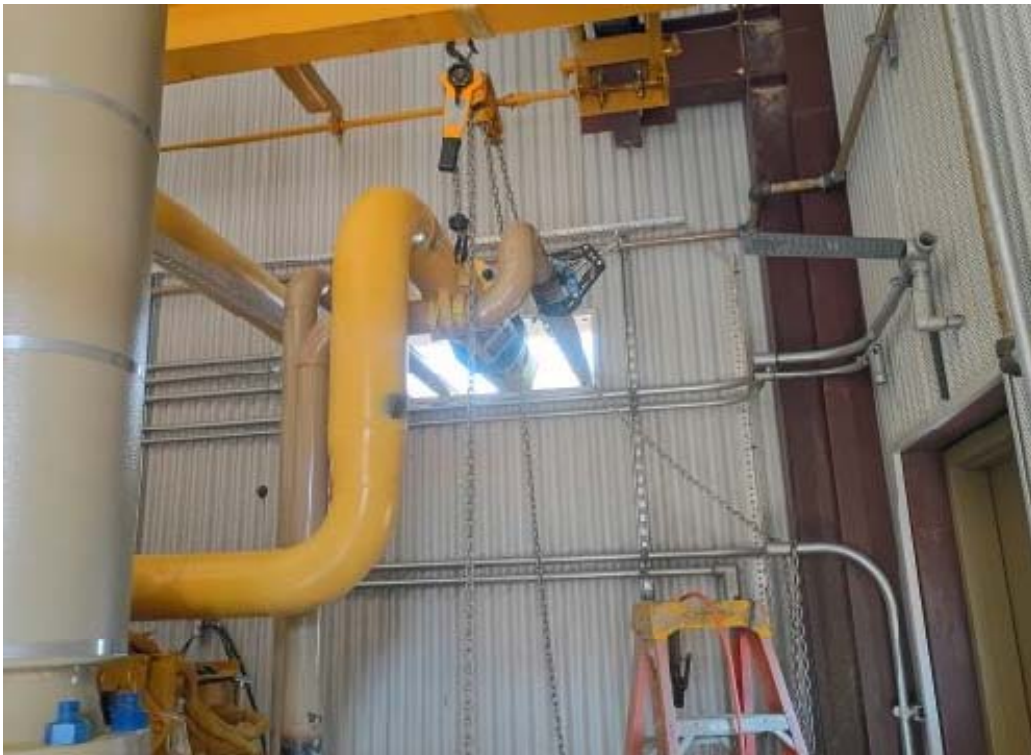
EL PASO NATURAL GAS COMPANY, L.L.C.

By /s/
Francisco Tarin
Director, Regulatory

Enclosures

Cc: Ms. Sareh Poormahdi, OEP

Weekly Status Report No. 35		
Docket No. CP24-520-000		
Project Name:	Maricopa Lateral Expansion Project	
County/State:	Yavapai County, Arizona	Date: 8/7/2026
Reporting Period:	July 26, 2026 to August 1, 2026	
Environmental Inspector:	Bobby Kimball	
1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD: During this period the contractor conducted the following activities: (i) continued pipe fabrication, x-raying, blasting and painting of pipe at various locations; (ii) continued pulling wires terminating at panel boxes; (iii) continued torquing of bolts; (iv) continued backfilling activities as applicable; (v) continued insulation of piping and tanks; (vi) continued verification checks of valves, actuators, flow meters and associated connections; (vii) installed the station septic system; (viii) poured concrete for pipe supports and air tank foundations; and (ix) began final grade activities of the site. 2. RELEVANT ENVIRONMENTAL ACTIVITIES: During this reporting period, the environmental inspector completed training for five (5) new personnel. Dust mitigation activities continued as necessary. 3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN: No environmental problems or issues occurred during this reporting period. 4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS: No environmental compliance issues or resolutions occurred during this reporting period. 5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS: No landowner issues or concerns were identified during this reporting period. 6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD: In the upcoming reporting period, the contractor will continue pipe fabrication, x-raying of pipe and setting forms. Electrical contractors will continue running conduit, cable trays and wiring. Contractor also plans to install remaining ancillary piping where applicable in the new compressor and auxiliary buildings. Trench backfilling activities will continue, as well as final grade work and verification checks.		

Maricopa Lateral Expansion Project Photo Documentation	
Location: Haystack Compressor Station site. Direction of Photo: North Date; 7/27/26 Description: Piping Insulation at the inlet filter separator.	
Location: Haystack Compressor Station site. Direction of Photo: East Date: 7/27/26 Description Pipe installation in the new compressor building.	

Location:
Haystack
Compressor
Station site.
**Direction of
Photo:**
East
Date: 7/28/26
Description
Setting forms
for the air tank
foundation.



Location:
Haystack
Compressor
Station site.
**Direction of
Photo:**
North
Date:
7/28/26
Description:
Insulation of
tanks.



Location:

Haystack
Compressor
Station site.

**Direction of
Photo:**

North

Date: 7/30/26

Description:

Final site grade
work.



Location:

Haystack
Compressor
Station site.

**Direction of
Photo:**

East

Date:

7/31/26

Description:

Installation of
field lines for
the new station
septic system.



Certificate of Service

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 7th day of August 2026.

/s/

Francisco Tarín

Two North Nevada Avenue
Colorado Springs, Colorado 80903
(719) 667-7517
