



November 8, 2024

Federal Energy Regulatory Commission  
888 First Street, N.E.  
Washington, D.C. 20426

Attention: Ms. Debbie-Anne Reese, Acting Secretary

Re: Wyoming Interstate Company, L.L.C.;  
Docket No. CP24-20-000,  
Cheyenne to Piceance Expansion Capacity Project  
Weekly Environmental Inspector Report No. 11

Commissioners:

Wyoming Interstate Company, L.L.C. (“WIC”) is hereby filing with the Federal Energy Regulatory Commission (“Commission”) in Docket No. CP24-20-000, its weekly status report related to WIC’s Cheyenne to Piceance Expansion Capacity Project (“Project”).

### **Description of Proceeding**

On November 29, 2023, WIC filed a prior notice request pursuant to Sections 157.205, 157.208 and 157.210 of the Commission’s regulations under the Natural Gas Act, and WIC’s blanket certificate issued in Docket No. CP83-22-000, for authorization to make certain modifications at its existing Wamsutter Compressor Station in Sweetwater County, Wyoming in order to generate incremental east to west firm natural gas transportation capacity of approximately 180,000 dekatherms per day on WIC’s mainline system.<sup>1</sup>

### **Submittal of Status Report**

In compliance with Section 157.208(c)(10) of the Natural Gas Act, WIC is providing Environmental Inspector Report No. 11.

### **Filing Information**

WIC is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

---

<sup>1</sup> On December 6, 2023, the Commission issued a Notice of Request Under Blanket Authorization initiating the 60-day comment period to allow for any person or Commission’s staff to file motions or notice to intervene and protests. Since no protests were filed within the comment period, the Project was deemed to be authorized on February 5, 2024.

Respectfully submitted,  
WYOMING INTERSTATE COMPANY,  
L.L.C.

By \_\_\_\_\_ /s/  
Francisco Tarin  
Director, Regulatory

Enclosures


Cc. Joel Cornwall, OEP

Wyoming Interstate Company, L.L.C.


<b>Wyoming Interstate Company, L.L.C. (WIC)</b>		
<b>WIC's Weekly Environmental Inspection Report No. 11</b>		
<b>Docket No. CP24-20-000</b>		
<b>Project Name:</b>	<b>Cheyenne to Piceance Expansion Capacity Project</b>	
<b>County/State:</b>	Sweetwater County, Wyoming	<b>Date:</b> 11/08/2024
<b>Reporting Period:</b>	October 27, 2024 through November 2, 2024	
<b>Environmental Inspector:</b>	Micah Hill	
<p><b>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</b> During this reporting period, crews poured concrete for the cooler footers and for the auxiliary building foundation then removed the forms. In addition, compressor unit one (1) suction and discharge line removal continued.</p> <p><b>2. RELEVANT ENVIRONMENTAL ACTIVITIES:</b> During this reporting period, the Environmental Inspector (EI) and WIC personnel provided environmental training to three (3) project personnel.</p> <p><b>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN:</b> No environmental problems/issues or corrective actions this reporting period.</p> <p><b>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS:</b> No environmental compliance issues or resolutions occurred during this reporting period.</p> <p><b>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS:</b> No landowner issues or concerns identified during this reporting period.</p> <p><b>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD:</b> Work planned for the next reporting period includes continued work to install forms and rebar for the gas cooler foundations, removal of existing pipe and fabrication of new pipe will continue, auxiliary building stem walls will be poured, and oil from compressor unit one (1) will be drained in preparation for removing the compressor.</p>		

Cheyenne to Piceance Expansion Capacity Project Photo Documentation

**Location:** Wamsutter Compressor Station  
**Direction of Photo:** Southeast  
**Description:** Pouring auxiliary building foundation wall  
**Date:** 10/28/2024

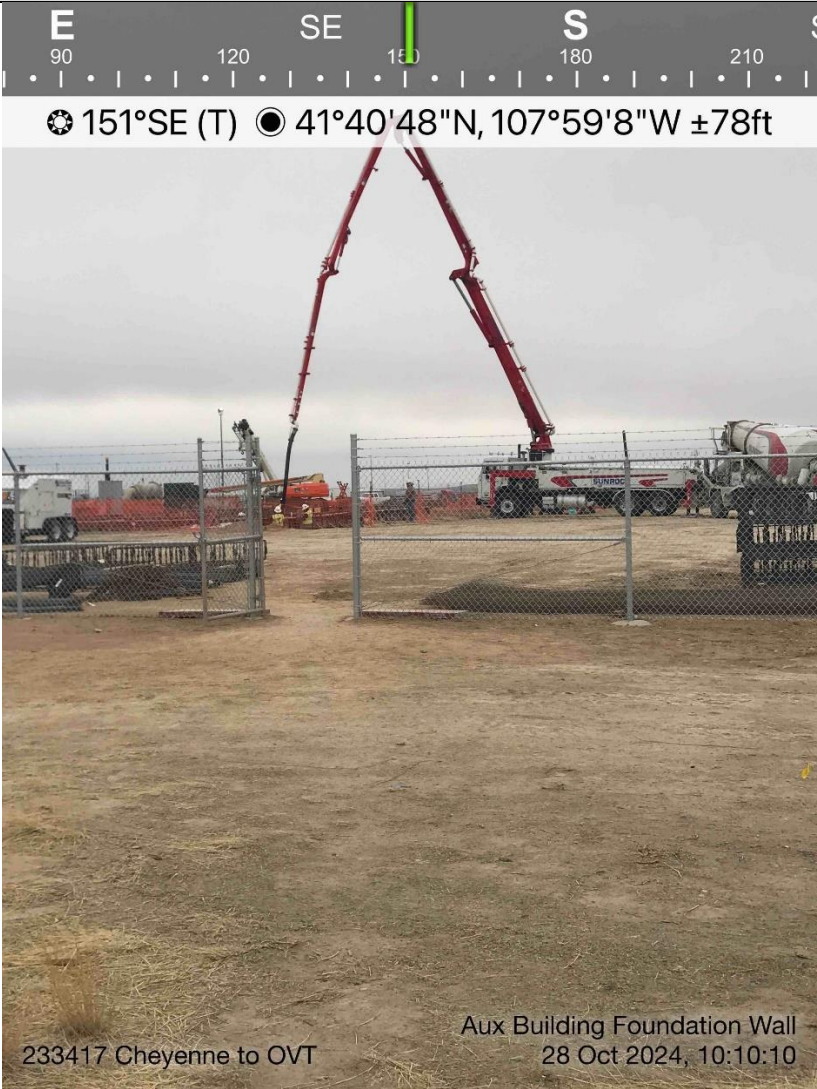

**Location:** Wamsutter  
Compressor Station  
**Direction of Photo:**  
Southeast  
**Description:** Forms  
removed from  
auxiliary walls  
**Date:** 11/2/2024

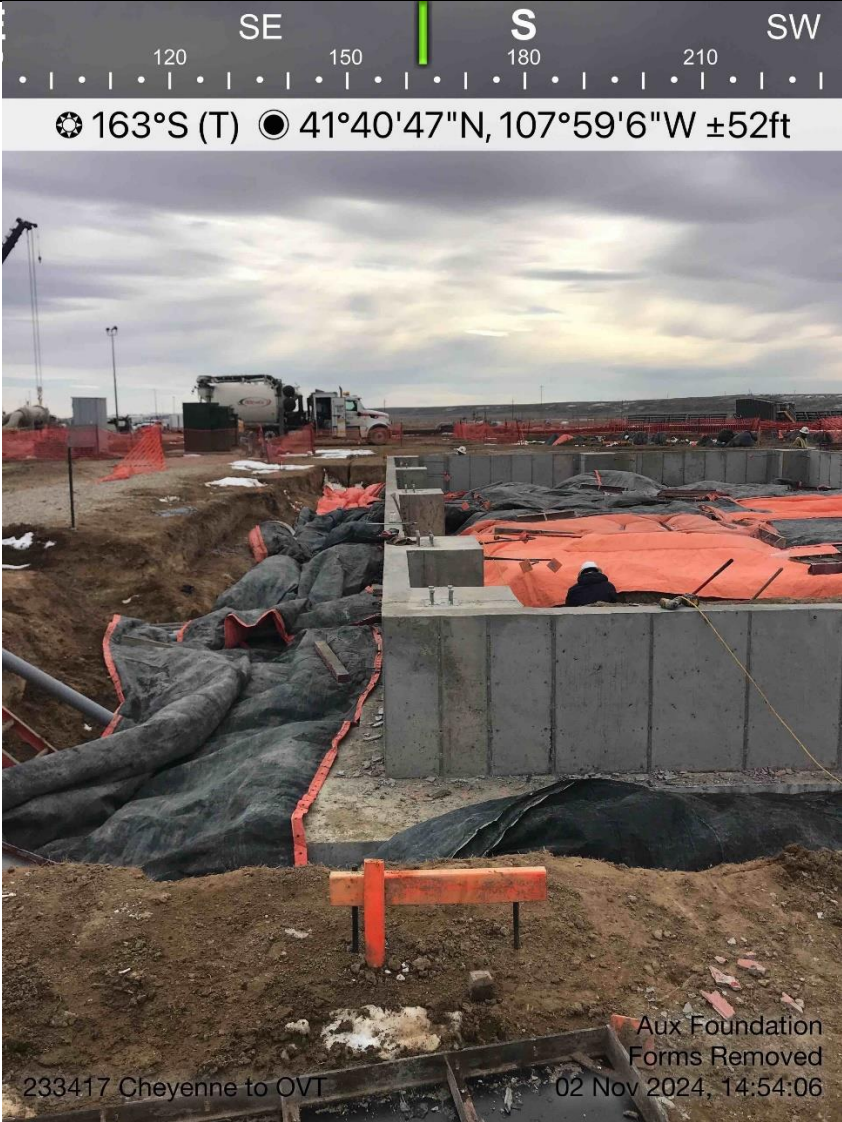



**Location:** Wamsutter  
Compressor Station  
**Direction of Photo:**  
Southwest  
**Description:**  
Removal of unit 1  
discharge piping  
**Date:** 11/2/2024



