

April 16, 2025

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne Reese, Secretary

Re: Wyoming Interstate Company, L.L.C.;
Docket No. CP24-20-000,
Cheyenne to Piceance Expansion Capacity Project
Weekly Environmental Inspector Report No. 34

Commissioners:

Wyoming Interstate Company, L.L.C. ("WIC") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP24-20-000, its weekly status report related to WIC's Cheyenne to Piceance Expansion Capacity Project ("Project").

Description of Proceeding

On November 29, 2023, WIC filed a prior notice request pursuant to Sections 157.205, 157.208 and 157.210 of the Commission's regulations under the Natural Gas Act, and WIC's blanket certificate issued in Docket No. CP83-22-000, for authorization to make certain modifications at its existing Wamsutter Compressor Station in Sweetwater County, Wyoming in order to generate incremental east to west firm natural gas transportation capacity of approximately 180,000 dekatherms per day on WIC's mainline system.¹

Submittal of Status Report

In compliance with Section 157.208(c)(10) of the Natural Gas Act, WIC is providing Environmental Inspector Report No. 34.

Filing Information

WIC is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

¹ On December 6, 2023, the Commission issued a Notice of Request Under Blanket Authorization initiating the 60-day comment period to allow for any person or Commission's staff to file motions or notice to intervene and protests. Since no protests were filed within the comment period, the Project was deemed to be authorized on February 5, 2024.

Wyoming Interstate Company, L.L.C. (WIC)		
WIC's Weekly Environmental Inspection Report No. 34		
Docket No. CP24-20-000		
Project Name:	Cheyenne to Piceance Expansion Capacity Project	
County/State:	Sweetwater County, Wyoming	Date: 4/16/2025
Reporting Period:	April 6, 2025 through April 12, 2025	
Environmental Inspector:	Micah Hill	
<p>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD: During this reporting period crews: (i) completed backfilling near auxiliary building 2 and for the emergency shut down lines, (ii) poured concrete for pipe supports and the recycle line, (iii) prepared forms and poured 9 yards of concrete for the separator pad, (iv) continued installing actuator valves, (v) slot trenched the kicker line and 2-inch emergency shutdown line, (vi) worked on above-grade conduit to the valves, and (vii) continued blasting and painting operations.</p> <p>2. RELEVANT ENVIRONMENTAL ACTIVITIES: During this reporting period, the Environmental Inspector (EI) and WIC personnel provided environmental training to one project personnel.</p> <p>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN: The silt fence around a new hydrovac waste pit was identified as being installed incorrectly and has since been installed properly.</p> <p>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS: No environmental compliance issues or resolutions occurred during this reporting period.</p> <p>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS: No landowner issues or concerns identified during this reporting period.</p> <p>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD: Work planned for the next reporting period includes: (i) continued high-pressure gas piping and actuator valve installation, (ii) anticipated completion of hydrotest section number 4, (iii) installing the 6-inch gas vent and emergency shut down line, (iv) installing the cooler risers, and (v) installing above-ground conduits to the valve settings.</p>		

Cheyenne to Piceance Expansion Capacity Project Photo Documentation

Location: Wamsutter
Compressor Station
Direction of Photo:
North
Description: Slot
trenching for the kicker
line.
Date: 4/7/2025




Location: Wamsutter
Compressor Station
Direction of Photo:
Southeast
Description: Poured
separator pad.
Date: 4/7/2025



Location: Wamsutter
Compressor Station
Direction of Photo:
North
Description: Backfilling
the fuel gas line.
Date: 4/7/2025



Location: Wamsutter
Compressor Station
Direction of Photo: East
Description: Properly
installed silt fence
around hydrovac waste
pit.
Date: 4/11/2025

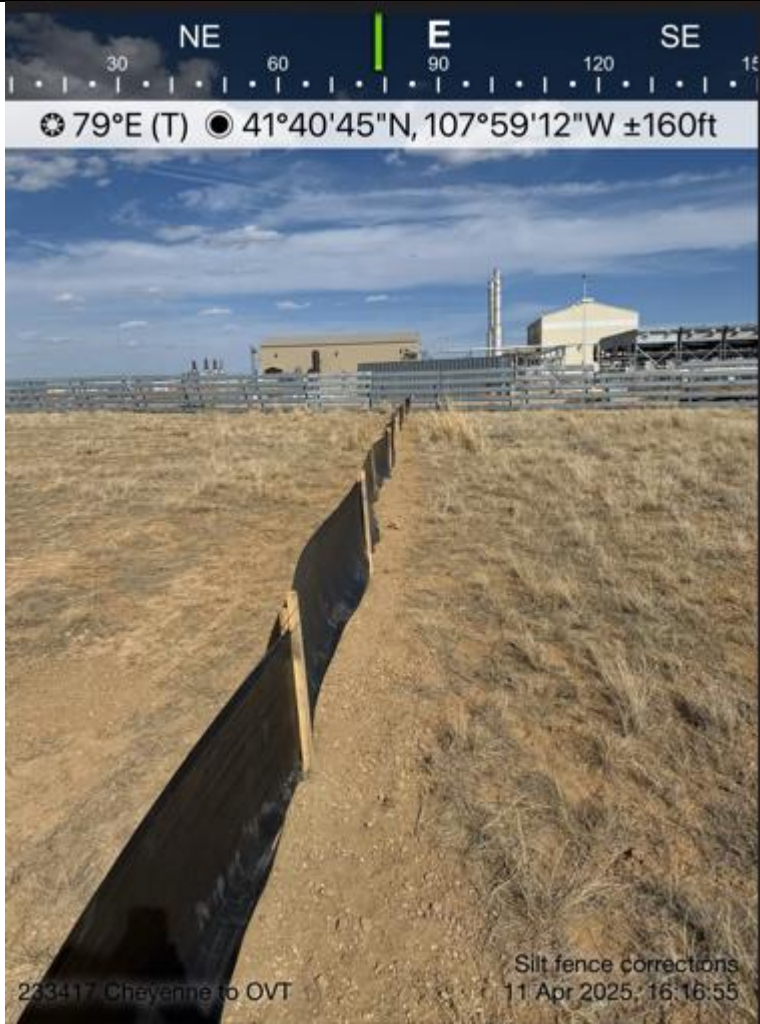

Certificate of Service

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 16th day of April 2025.

/s/

Francisco Tarin

Two North Nevada Avenue
Colorado Springs, Colorado 80903
(719) 667-7517
