

May 23, 2019

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Kimberly D. Bose, Secretary

Re: Colorado Interstate Gas Company, L.L.C.
Docket No. CP19-56-000
CIG High Plains Kiowa Lateral Expansion Project
Weekly Environmental Inspector Report No. 5

Commissioners:

Colorado Interstate Gas Company, L.L.C. ("CIG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP19-56-000 its Weekly Environmental Inspector Report related to the CIG High Plains Kiowa Lateral Expansion Project.

Description of Proceeding

On January 24, 2019, CIG filed a prior notice request to Sections 157.205(b), 157.208(b), and 157.210 of the Commission's Regulations under the Natural Gas Act for authorization to construct and operate two laterals and metering facilities located in Weld County, Colorado. The project is referred to as the "CIG High Plains Kiowa Lateral Expansion Project".

Submittal of Environmental Inspector Report

In compliance with Section 157.208(c)(10) of the Natural Gas Act, CIG is providing Environmental Inspector Report No. 5 for the period of May 12, 2019 through May 18, 2019.

Filing Information

CIG is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

Respectfully submitted,
COLORADO INTERSTATE GAS COMPANY,
L.L.C.

By /s/
Francisco Tarin
Director, Regulatory

Enclosure



CIG Weekly Environmental Inspector Report No. 5		
Docket No. CP19-56-000		
Project Name:	CIG High Plains Kiowa Lateral Expansion Project	
County/State:	Weld County, Colorado	Date: 5/23/2019
Reporting Period:	May 12, 2019 to May 18, 2019	
Environmental Inspector:	Ken Lupi	

1. Summary of Construction Activity for Inspection Period:
During this reporting period, the construction contractor continued with topsoil stripping, ditching, and pipe stringing on the High Five Lateral. The pipe was laid in and backfilled from STA. 2+08 to STA. 25+41. The cultural monitor was onsite for the open trench inspection. Topsoil stripping on the ditch line and portions of the working side of the ROW were completed on the Kiowa Lateral. The pad was graded for the High Five Meter Station. Fabrication work continued at the Prairie Hound Meter Station.

2. Relevant Environmental Activities:
During this reporting period, forty-seven (47) people received environmental training. A total of one-hundred and thirteen (113) people have received training on the CIG High Plains Kiowa Lateral Expansion Project.

At the wetland located at STA. 473+92, work continued on the equipment bridge. The wetland boundaries between STA. 375+00 and STA. 365+00 were surveyed and silt fence was installed. A cultural site was identified during the topsoil removal on the Kiowa Lateral. Archeologists are onsite conducting testing to determine eligibility. The final determination is expected during the next reporting period. Erosion control devices were installed throughout the project as necessary.

3. Environmental Problems/Issues and Corrective Actions Taken:
There were no environmental problems or issues identified during this reporting period.

4. Environmental Compliance Issues/Resolutions:
There were no environmental compliance issues identified during this reporting period.

5. Issues and Concerns Identified by Landowners:
No landowner issues or concerns were identified during this reporting period.

6. Work Planned for the Following Reporting Period:
It is anticipated during the next reporting period that the construction contractor will complete backfilling on the High Five Lateral. On the Kiowa Lateral the construction contractor will continue ditching, stringing, bending and welding pipe. It is expected that the foundation and



Colorado Interstate
Gas Company, L.L.C.
a Kinder Morgan company

civil work will be complete on the High Five Meter Station. The construction contractor will prepare for the hydrotest on the Prairie Hound Meter Station.



Report No. 5

Photos

Location: STA
473+92
**Direction of
Photo:** East
Description:
Wetland crossing



Location: STA
473+92
**Direction of
Photo:** West
Description: Silt
fence installed at
the wetland.






Photos

Location: STA
473+92
**Direction of
Photo:** North
Description: Silt
Fence installation



Location: STA
473+92
**Direction of
Photo:** North
Description:
Slope breaker and
outfall structure
installed.

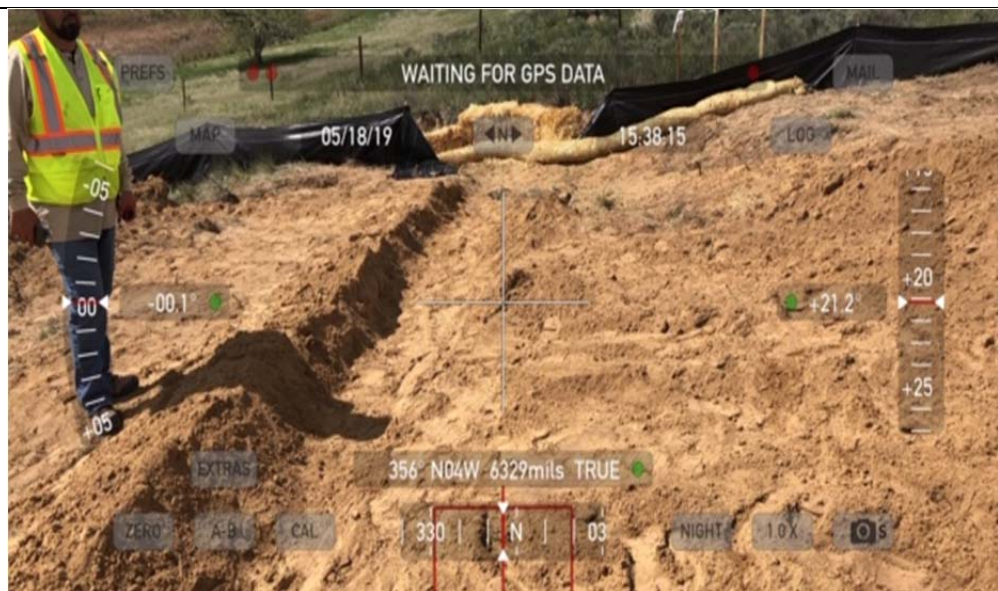



Photos

Location: Kiowa
Lateral approx.
STA 400+00

**Direction of
Photo:** West


Description:
Grader stripping
topsoil from the
working side of
ROW



Location: High
Five Meter Station

**Direction of
Photo:** East

Description:
Applying gravel to
the pad site.

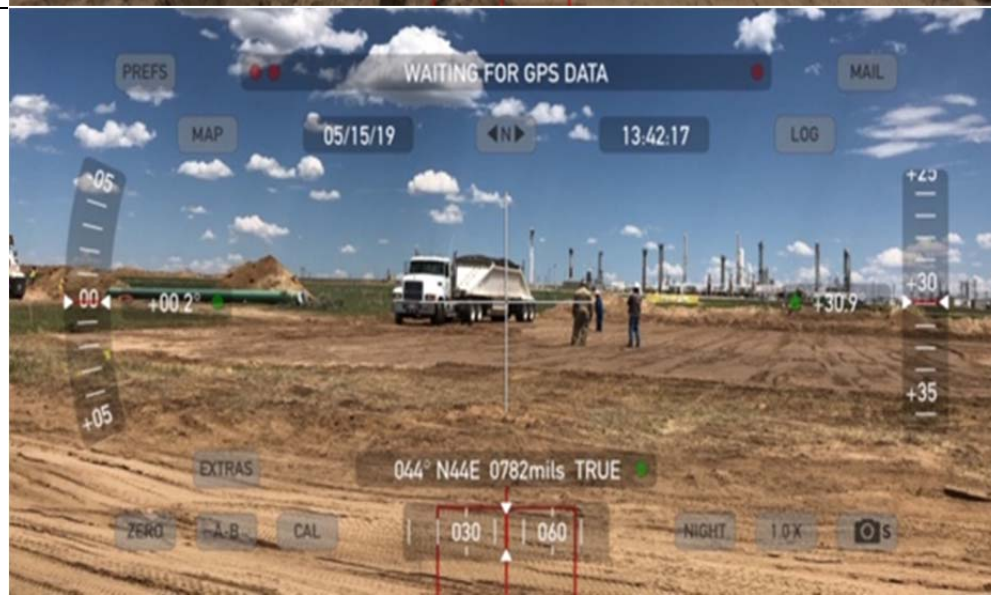

Certificate of Service

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 23rd day of May, 2019.

/s/

Francisco Tarin

Two North Nevada Avenue
Colorado Springs, Colorado 80903
(719) 667-7517
