



July 11, 2024

Federal Energy Regulatory Commission  
888 First Street, N.E.  
Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Acting Secretary

Re: El Paso Natural Gas Company, L.L.C.;  
Docket No. CP23-546-000  
Line No. 1110 Loop Project  
Weekly Environmental Inspector Report – July 1, 2024 through July 7, 2024

Commissioners:

El Paso Natural Gas Company, L.L.C. ("EPNG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP23-546-000, its weekly status report related to the Line No. 1110 Loop Project ("Project").

### **Description of Proceeding**

On September 22, 2023, EPNG submitted a Request for Prior Notice Authorization Pursuant to Blanket Certificate in the above-referenced docket seeking authorization to construct, install, operate and maintain an approximately two-mile 30-inch outside diameter pipeline loop extension, located in Hudspeth County, Texas as part of its Line No. 1110 Loop Project.<sup>1</sup>

### **Submittal of Status Report**

In compliance with Section 157.208(c)(10) of the Natural Gas Act, EPNG is providing Environmental Inspector Report for the period of July 1, 2024 through July 7, 2024.

---

<sup>1</sup> EPNG received a timely protest within 60-days of the date of the notice issued by the Commission. Accordingly, the Project was reviewed as a case-specific certificate application under section 7 of the NGA. On April 25, 2024, the Commission issued an order denying the protest and authorizing EPNG to construct and operate the proposed facilities under its Part 157 blanket certificate.



**Certificate of Service**

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 11<sup>th</sup> day of July 2024.

*/s/*

---


Francisco Tarin

Two North Nevada Avenue  
Colorado Springs, Colorado 80903  
(719) 667-7517


<b>EPNG's Weekly Environmental Inspection Report No. 8</b>		
<b>Docket No. CP23-546-000</b>		
<b>Project Name:</b>	<b>Line No. 1110 Loop Project</b>	
<b>County/State:</b>	Hudspeth County, Texas	<b>Date:</b> 07/11/2024
<b>Reporting Period:</b>	07/01/2024 – 07/07/2024	
<b>Environmental Inspection:</b>	Chennie Castanon	
<p><b>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</b></p> <ul style="list-style-type: none"> <li>• Continued welding and bolt-up activities on launcher assembly.</li> <li>• Completed x-raying pipe joints.</li> <li>• Continued lowering mainline pipe into trench and backfilling.</li> <li>• Continued hauling water for the hydrostatic testing activities to the frac tanks.</li> <li>• Completed hydrostatic testing activities on the western half of the mainline pipe.</li> <li>• Started restoration and cleanup activities.</li> </ul> <p><b>2. RELEVANT ENVIRONMENTAL ACTIVITIES:</b>  During this reporting period, the Environmental Inspector (EI) conducted a Stormwater Pollution Prevention Plan (SWPPP) inspection after the project area received 0.90-inch of rainfall and also conducted daily surveys for sensitive species along the access route and project workspaces.</p> <p><b>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN:</b>  No environmental problems/issues or corrective actions this reporting period.</p> <p><b>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS:</b>  No environmental compliance issues or resolutions occurred during this reporting period.</p> <p><b>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS:</b>  No landowner issues or concerns identified during this reporting period.</p> <p><b>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD:</b>  Construction contractor will: continue restoration and cleanup activities, complete lowering pipe into trench, complete installation of relocated launcher, and complete hydrostatic testing activities.</p>		

**Line No. 1110 Loop Project**

**Location:** MP 53+00  
**Direction of Photo:** Southwest  
**Description:** Contractors launching cleaning pigs to internally clean pipe.  
**Date:** 07/02/2024

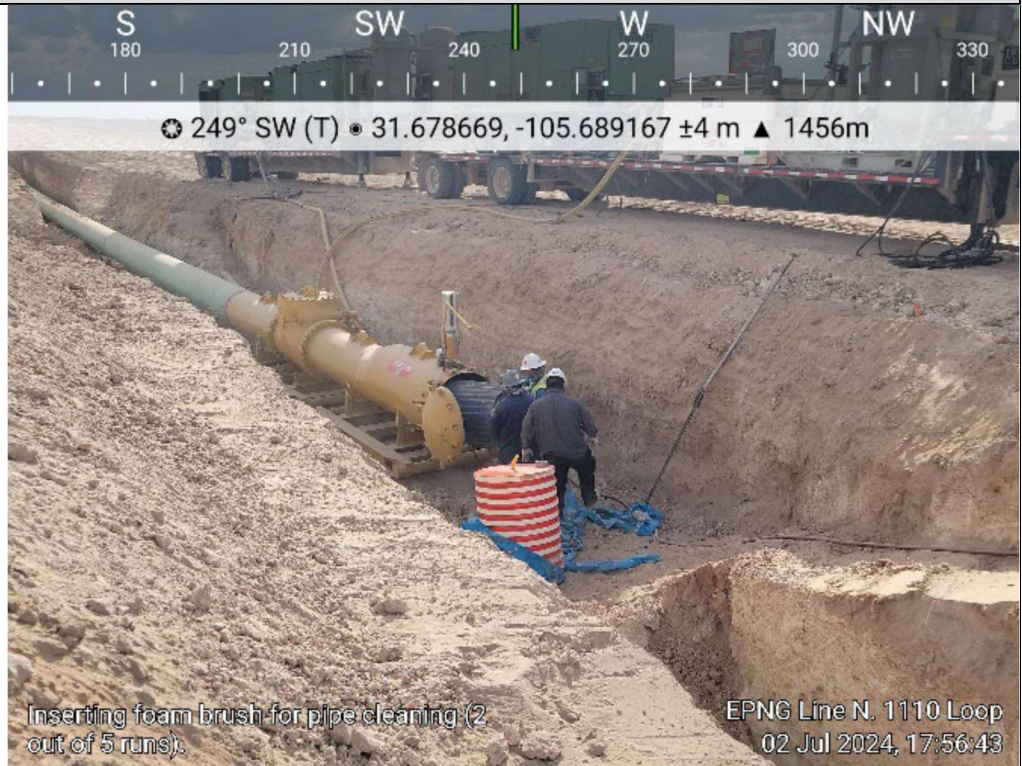

**Location:** MP 65+00  
**Direction of Photo:** West  
**Description:** Crews cleaning up right-of-way.  
**Date:** 07/05/2024

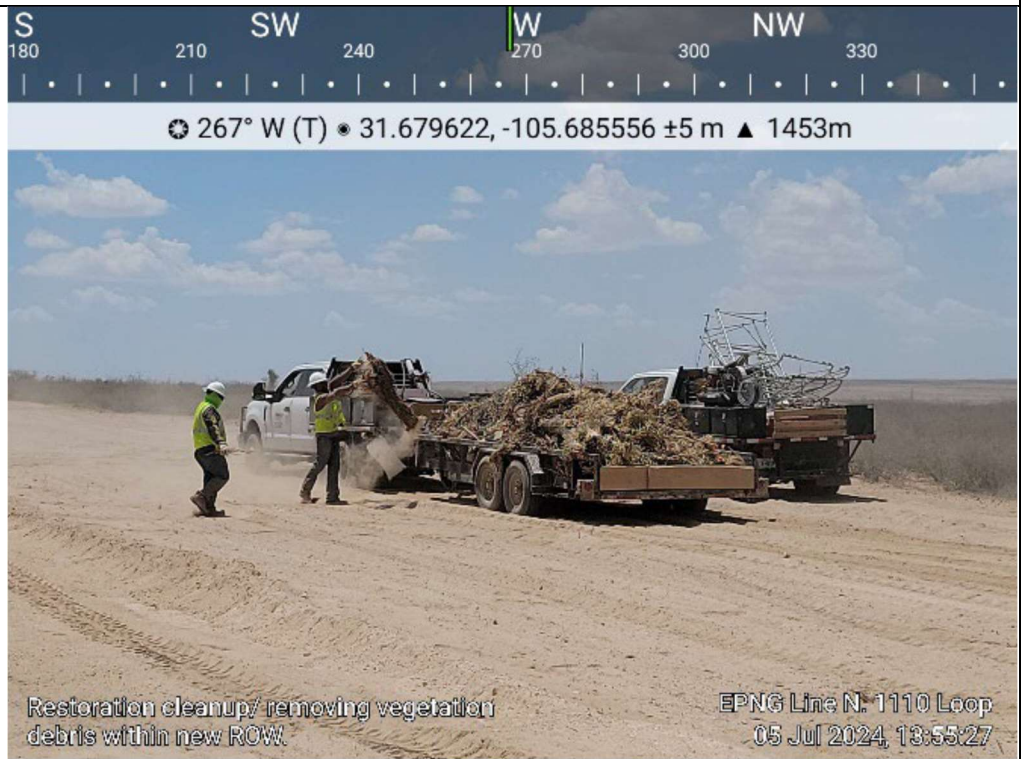

**Line No. 1110 Loop Project**

**Location:** MP 0+00  
**Direction of Photo:**  
North  
**Description:** Hydrostatic testing equipment in use.  
**Date:** 07/05/2024



**Location:** MP 105+00  
**Direction of Photo:**  
South  
**Description:** Installation of bolt-up piping on pig launcher assembly.  
**Date:** 07/02/2024

