



August 1, 2024

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Acting Secretary

Re: El Paso Natural Gas Company, L.L.C.;
Docket No. CP23-546-000
Line No. 1110 Loop Project
Weekly Environmental Inspector Report – July 22, 2024 through July 28, 2024

Commissioners:

El Paso Natural Gas Company, L.L.C. ("EPNG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP23-546-000, its weekly status report related to the Line No. 1110 Loop Project ("Project").

Description of Proceeding

On September 22, 2023, EPNG submitted a Request for Prior Notice Authorization Pursuant to Blanket Certificate in the above-referenced docket seeking authorization to construct, install, operate and maintain an approximately two-mile 30-inch outside diameter pipeline loop extension, located in Hudspeth County, Texas as part of its Line No. 1110 Loop Project.¹

Submittal of Status Report

In compliance with Section 157.208(c)(10) of the Natural Gas Act, EPNG is providing Environmental Inspector Report for the period of July 22, 2024 through July 28, 2024.

¹ EPNG received a timely protest within 60-days of the date of the notice issued by the Commission. Accordingly, the Project was reviewed as a case-specific certificate application under section 7 of the NGA. On April 25, 2024, the Commission issued an order denying the protest and authorizing EPNG to construct and operate the proposed facilities under its Part 157 blanket certificate.

Filing Information

EPNG is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

Respectfully submitted,

EL PASO NATURAL GAS COMPANY, L.L.C.

By _____/s/
Francisco Tarin
Director, Regulatory

Enclosures

Certificate of Service

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 1st day of August 2024.

/s/


Francisco Tarin

Two North Nevada Avenue
Colorado Springs, Colorado 80903
(719) 667-7517

EPNG's Weekly Environmental Inspection Report No. 11		
Docket No. CP23-546-000		
Project Name:	Line No. 1110 Loop Project	
County/State:	Hudspeth County, Texas	Date: 08/1/2024
Reporting Period:	07/22/2024 – 07/28/2024	
Environmental Inspection:	Chennie Castanon	
<p>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</p> <ul style="list-style-type: none"> • Completed blasting and coating the relocated pig launcher. • Completed backfilling and grading at the pig launcher site. • Completed discharging hydrostatic test water from frac tanks. • Started installing security fencing around relocated pig launcher. • Continued restoration and cleanup activities at pig launcher site, along new ROW for mainline pipe, and along access route. <p>2. RELEVANT ENVIRONMENTAL ACTIVITIES: During this reporting period, the Environmental Inspector (EI) observed the discharge of hydrostatic test water.</p> <p>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN: No environmental problems/issues or corrective actions this reporting period.</p> <p>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS: No environmental compliance issues or resolutions occurred during this reporting period.</p> <p>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS: No landowner issues or concerns identified during this reporting period.</p> <p>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD: Construction contractor will: Continue restoration and cleanup activities and start seeding the ROW and workspaces.</p>		

Line No. 1110 Loop Project

Location: MP 0+00
Direction of Photo: North
Description: Western terminus of the project area restored to original grade.
Date: 07/23/2024

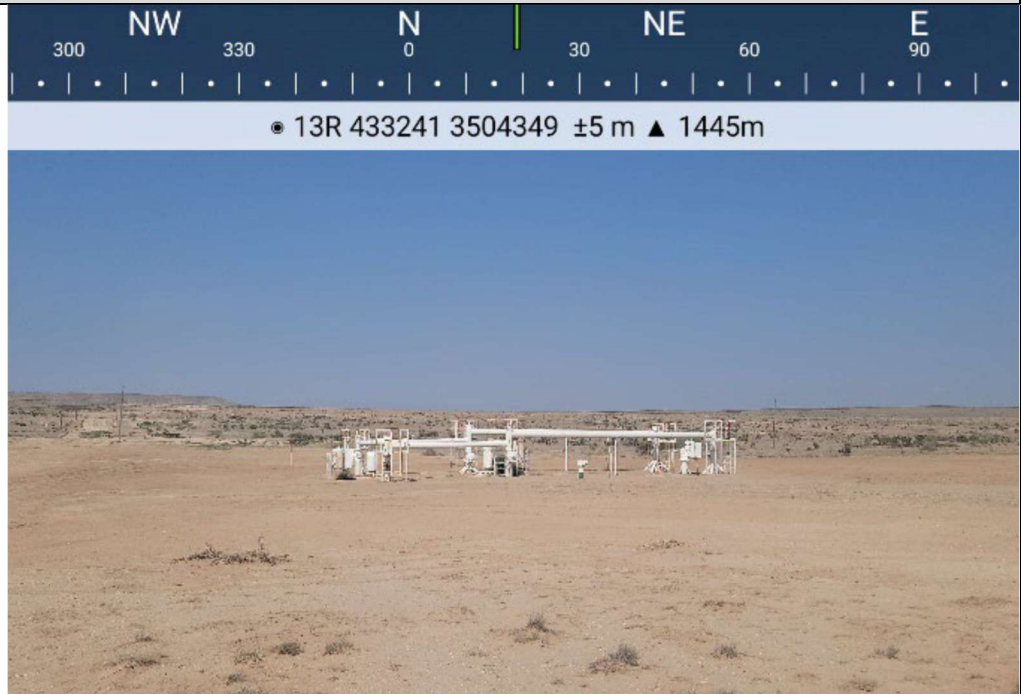

Location: Additional Temporary Workspace Immediately North of MP 53+00
Direction of Photo: Southwest
Description: Hydrostatic test water discharge structure.
Date: 07/24/2024



Line No. 1110 Loop Project

Location: Access Route
PAR #02
Direction of Photo:
Southwest
Description: Completed
restoration on portion
of access route PAR #02.
Date: 07/24/2024

