



July 19, 2024

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Acting Secretary

Re: El Paso Natural Gas Company, L.L.C.;
Docket No. CP23-546-000
Line No. 1110 Loop Project
Weekly Environmental Inspector Report – July 8, 2024 through July 14, 2024

Commissioners:

El Paso Natural Gas Company, L.L.C. ("EPNG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP23-546-000, its weekly status report related to the Line No. 1110 Loop Project ("Project").

Description of Proceeding

On September 22, 2023, EPNG submitted a Request for Prior Notice Authorization Pursuant to Blanket Certificate in the above-referenced docket seeking authorization to construct, install, operate and maintain an approximately two-mile 30-inch outside diameter pipeline loop extension, located in Hudspeth County, Texas as part of its Line No. 1110 Loop Project.¹

Submittal of Status Report

In compliance with Section 157.208(c)(10) of the Natural Gas Act, EPNG is providing Environmental Inspector Report for the period of July 8, 2024 through July 14, 2024.

¹ EPNG received a timely protest within 60-days of the date of the notice issued by the Commission. Accordingly, the Project was reviewed as a case-specific certificate application under section 7 of the NGA. On April 25, 2024, the Commission issued an order denying the protest and authorizing EPNG to construct and operate the proposed facilities under its Part 157 blanket certificate.

Certificate of Service

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 19th day of July 2024.

/s/


Francisco Tarin

Two North Nevada Avenue
Colorado Springs, Colorado 80903
(719) 667-7517

EPNG's Weekly Environmental Inspection Report No. 9		
Docket No. CP23-546-000		
Project Name:	Line No. 1110 Loop Project	
County/State:	Hudspeth County, Texas	Date: 07/19/2024
Reporting Period:	07/08/2024 – 07/14/2024	
Environmental Inspection:	Chennie Castanon	
<p>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</p> <ul style="list-style-type: none"> • Completed hydrostatic testing activities on the mainline pipe and launcher assembly. • Completed lowering mainline pipe into trench and backfilling. • Continued restoration and cleanup activities. <p>2. RELEVANT ENVIRONMENTAL ACTIVITIES:</p> <p>During this reporting period, the Environmental Inspector (EI) conducted a Stormwater Pollution Prevention Plan (SWPPP) inspection after the project area received 0.50-inch of rainfall and also conducted daily surveys for sensitive species along the access route and project workspaces. Eleven box turtles were found on PAR #02 and relocated. EI placed additional signage to warn for presence of wildlife due to presence of numerous box turtles.</p> <p>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN:</p> <p>No environmental problems/issues or corrective actions this reporting period.</p> <p>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS:</p> <p>No environmental compliance issues or resolutions occurred during this reporting period.</p> <p>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS:</p> <p>No landowner issues or concerns identified during this reporting period.</p> <p>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD:</p> <p>Construction contractor will: dry mainline and launcher assembly piping, continue restoration and cleanup activities and discharge hydrostatic test water from frac tanks. Commissioning of the pipe is anticipated to occur.</p>		

Line No. 1110 Loop Project

Location: MP 53+00
Direction of Photo: Southwest
Description: Hydrostatic test water transferred from one pipe segment to another segment.
Date: 07/08/2024

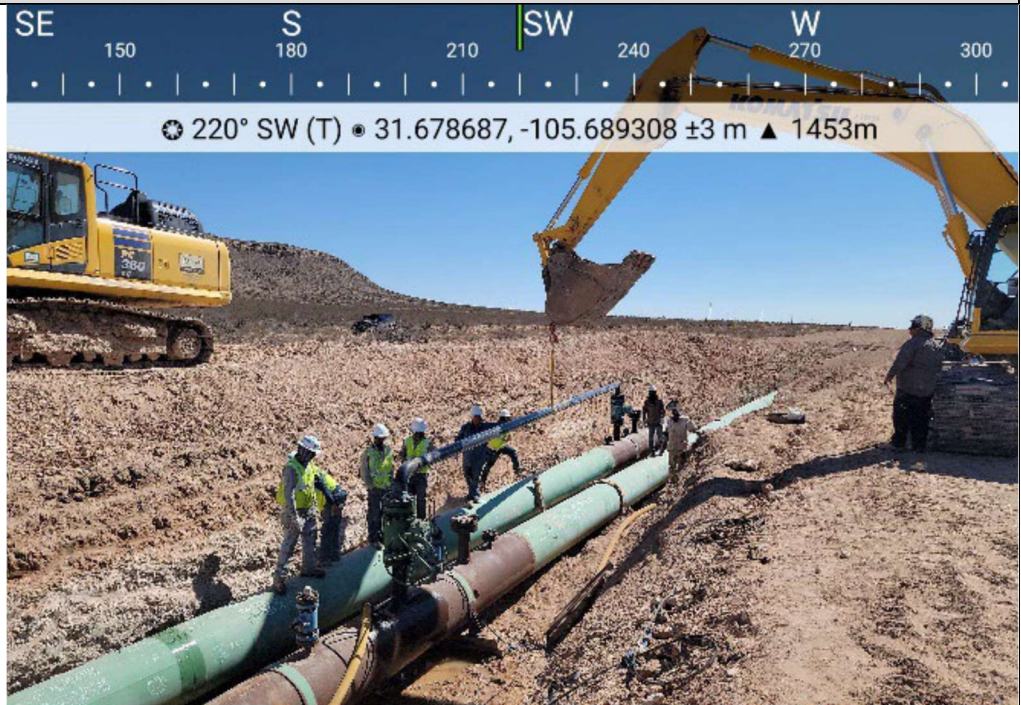

Location: Access Road PAR #02
Direction of Photo: Northwest
Description: Additional signage placed to watch for wildlife.
Date: 07/08/2024



Line No. 1110 Loop Project

Location: MP 6+90
Direction of Photo:
Northwest
Description: Installation
of permanent slope
breaker on new ROW as
part of restoration
activities.
Date: 07/12/2024

