



July 3, 2024

Federal Energy Regulatory Commission  
888 First Street, N.E.  
Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Acting Secretary

Re: El Paso Natural Gas Company, L.L.C.;  
Docket No. CP23-546-000  
Line No. 1110 Loop Project  
Weekly Environmental Inspector Report – June 24, 2024 through June 30, 2024

Commissioners:

El Paso Natural Gas Company, L.L.C. ("EPNG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP23-546-000, its weekly status report related to the Line No. 1110 Loop Project ("Project").

### **Description of Proceeding**

On September 22, 2023, EPNG submitted a Request for Prior Notice Authorization Pursuant to Blanket Certificate in the above-referenced docket seeking authorization to construct, install, operate and maintain an approximately two-mile 30-inch outside diameter pipeline loop extension, located in Hudspeth County, Texas as part of its Line No. 1110 Loop Project.<sup>1</sup>

### **Submittal of Status Report**

In compliance with Section 157.208(c)(10) of the Natural Gas Act, EPNG is providing Environmental Inspector Report for the period of June 24, 2024 through June 30, 2024.

---

<sup>1</sup> EPNG received a timely protest within 60-days of the date of the notice issued by the Commission. Accordingly, the Project was reviewed as a case-specific certificate application under section 7 of the NGA. On April 25, 2024, the Commission issued an order denying the protest and authorizing EPNG to construct and operate the proposed facilities under its Part 157 blanket certificate.

**Filing Information**

EPNG is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

Respectfully submitted,

EL PASO NATURAL GAS COMPANY, L.L.C.

By \_\_\_\_\_ /s/  
Francisco Tarin  
Director, Regulatory

Enclosures

**Certificate of Service**

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 3<sup>rd</sup> day of July 2024.

*/s/*

\_\_\_\_\_  
Francisco Tarin

Two North Nevada Avenue  
Colorado Springs, Colorado 80903  
(719) 667-7517

<b>EPNG's Weekly Environmental Inspection Report No. 5</b>		
<b>Docket No. CP23-546-000</b>		
<b>Project Name:</b>	<b>Line No. 1110 Loop Project</b>	
<b>County/State:</b>	Hudspeth County, Texas	<b>Date:</b> 07/03/2024
<b>Reporting Period:</b>	06/24/2024 – 06/30/2024	
<b>Environmental Inspection:</b>	Chennie Castanon	
<p><b>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</b></p> <ul style="list-style-type: none"> <li>• Completed work on foundations for launcher relocation and started installing launcher.</li> <li>• Continued x-raying pipe joints.</li> <li>• Continued trenching for mainline pipe and started lowering mainline pipe into trench.</li> <li>• Continued to grade along access road and applied water for dust suppression where necessary.</li> <li>• Started delivering frac tanks and water to the right-of-way in preparation for hydrostatic testing activities.</li> </ul> <p><b>2. RELEVANT ENVIRONMENTAL ACTIVITIES:</b>  During this reporting period, the Environmental Inspector (EI) conducted a Stormwater Pollution Prevention Plan (SWPPP) inspection after the project area received 0.50-inch of rainfall and also conducted daily surveys for sensitive species along the access route and project workspaces.</p> <p><b>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN:</b>  No environmental problems/issues or corrective actions this reporting period.</p> <p><b>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS:</b>  No environmental compliance issues or resolutions occurred during this reporting period.</p> <p><b>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS:</b>  No landowner issues or concerns identified during this reporting period.</p> <p><b>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD:</b>  Construction contractor will: continue grading activities along the access road, complete x-raying pipe, complete ditching and lowering pipe into trench, complete installation of relocated launcher, and begin hydrostatic testing activities.</p>		

**Line No. 1110 Loop Project**

**Location:** MP 99+60  
**Direction of Photo:**  
Southwest  
**Description:** Pipeline  
trench with pipe on  
supports.  
**Date:** 06/24/2024




**Location:** MP 37+00  
**Direction of Photo:** East  
**Description:** Pipe being  
lowered into the trench.  
**Date:** 06/26/2024



**Line No. 1110 Loop Project**

**Location:** Immediately north of MP 53+00 within additional temporary workspace.  
**Direction of Photo:** West  
**Description:** Water being delivered and stored in frac tanks for hydrostatic testing activities.  
**Date:** 06/28/2024

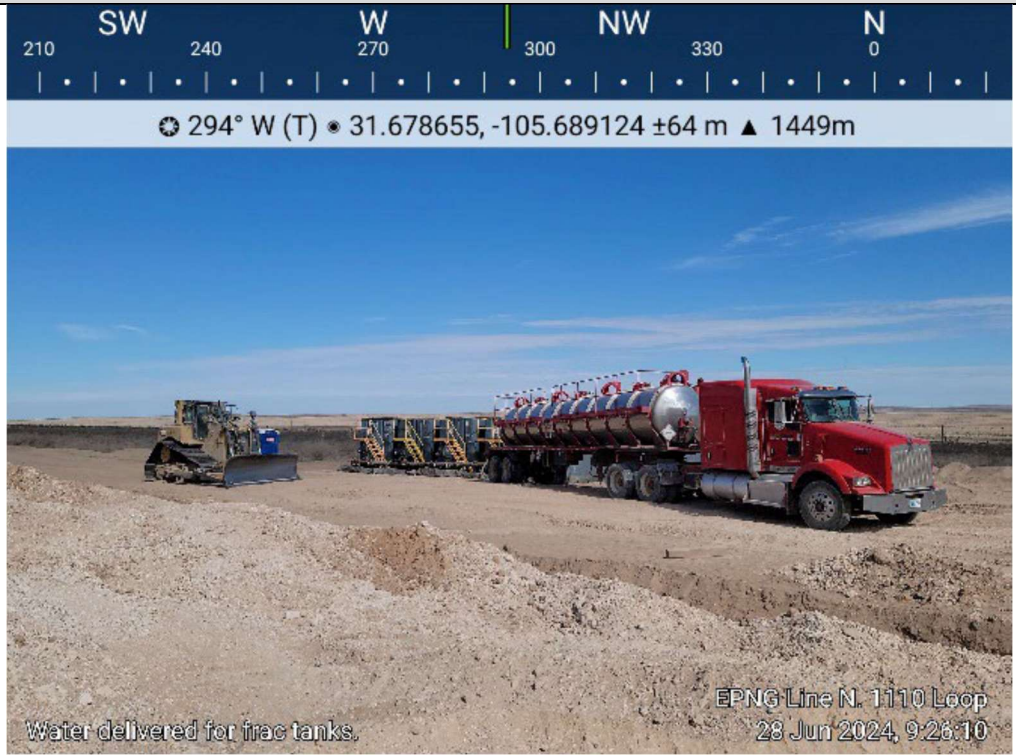

**Location:** MP 105+00  
**Direction of Photo:** North  
**Description:** Installation of pig launcher assembly.  
**Date:** 06/28/2024

