

February 2, 2023

Federal Energy Regulatory Commission 888 First Street, N.E. Washington, D.C. 20426

Attention: Ms. Kimberly D. Bose, Secretary

Re: Mojave Pipeline Company, L.L.C.;

Docket No. CP21-495-000,

Weekly Environmental Inspector Report No. 17

Dear Ms. Bose:

Mojave Pipeline Company, L.L.C. ("Mojave") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP21-495-000, its weekly status report related to the Oak Creek Delivery Point Project ("Project").

Description of Proceeding

On September 13, 2021, Mojave filed a prior notice request pursuant to Sections 157.203, 157.205, and 157.211 of the Commission's regulations under the Natural Gas Act for authorization to construct the Oak Creek Delivery Point located in Kern County, California. On September 23, 2021, the Commission issued a Notice of Request Under Blanket Authorization initiating the 60 day comment period to allow for any person or Commission's staff to file motions or notice to intervene and protests. Since no protests were filed within the comment period, the Project was deemed to be authorized on November 23, 2021.

Submittal of Status Report

Mojave is herein providing Environmental Inspector Report No. 17 for the period of January 22, 2023 through January 31, 2023.

Filing Information

Mojave is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

MOJA	VE PIPELINE COMPANY, L.L.C.
Ву	/s/
	Francisco Tarin Director, Regulatory
	Director, regulatory

Respectfully submitted,

Cc: Mr. Danny Laffoon



Mojave Weekly Environmental Inspector Report No. 17			
Docket No. CP21-495-000			
Project Name:	Oak Creek Delivery Point Project		
County/State:	Kern County, California	Date: 01/31/23	
Reporting Period:	January 22, 2023, to January 31, 2023		
Environmental	Charles Wisenor		
Inspector/			
Chief Inspector:			

- 1. Summary of Construction Activity for Inspection Period: Only With the exception of painting and completion of minor punch-list activities items, Michels Pipeline, Inc. ("Michels"), Mojave and CalPortland's construction contractor, completed work at the Mojave Oak Creek Delivery tap site. The Mojave Oak Creek Delivery Tap is now mechanically complete and ready for service. Michels also completed installation of the electronic gas measurement bus stop panel at the CalPortland Meter Station as well as setting of the new meter and flow control mechanism. Deliveries to CalPortland will commence upon completion of its downstream meter station facilities.
- **2. Relevant Environmental Activities:** There were no environmental activities or training that took place during this reporting period.
- **3. Environmental Problems/Issues and Corrective Actions Taken:** There were no environmental problems or issues identified during this reporting period.
- **4. Environmental Compliance Issues/Resolutions:** There were no environmental compliance issues identified during this reporting period.
- 5. Issues and Concerns Identified by Landowners:

 There were no landowner issues or concerns were reported during this reporting period.
- **6.** Work Planned for the Following Reporting Period: During the next reporting period, it is anticipated that Michels will continue remaining items for CalPortland's portion of the project to include running wire to hook up the meter and the flow control mechanism, completing the grounding grid, painting, fencing and graveling. Michels will finish remaining painting activities at the Mojave Oak Creek Delivery tap site.



Report No. 17

Photos

Date: 01/30/2023

Location: Mojave Oak Creek

Delivery Tap

Direction of Photo: North **Description:** View of piers and restoration at the Oak Creek Delivery tap site.



Date: 01/30/2023

Location: Mojave Oak Creek

Delivery Tap

Direction of Photo: West **Description:** View of crew spreading gravel at the Oak Creek Delivery tap site.





Photos

Date: 01/31/2023

Location: Mojave Oak Creek

Delivery Tap

Direction of Photo: East **Description:** View of the mechanically complete Oak

Creek Delivery tap.



Date: 01/31/2023

Location: CalPortland-owned


Meter Station Site

Direction of Photo:

Northeast

Description: View of the bus

stop panel.

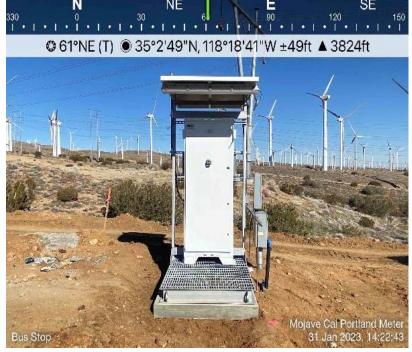



Photos

Date: 01/31/2023 Location: CalPortlandowned Meter Station Site Direction of Photo:

Northwest

Description: View of the flow control and meter skids in place at the CalPortland meter site.




Date: 01/23/2023 Location: CalPortlandowned Meter Station Site Direction of Photo: North Description: View of electrical contractor installing gauges on the flow control skid.



Certificate of Service

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 2nd day of February 2023.



Two North Nevada Avenue Colorado Springs, Colorado 80903 (719) 667-7517
