



June 20, 2024

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Acting Secretary

Re: El Paso Natural Gas Company, L.L.C.;
Docket No. CP23-546-000
Line No. 1110 Loop Project
Weekly Environmental Inspector Report – June 10, 2024 through June 16, 2024

Commissioners:

El Paso Natural Gas Company, L.L.C. ("EPNG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP23-546-000, its weekly status report related to the Line No. 1110 Loop Project ("Project").

Description of Proceeding

On September 22, 2023, EPNG submitted a Request for Prior Notice Authorization Pursuant to Blanket Certificate in the above-referenced docket seeking authorization to construct, install, operate and maintain an approximately two-mile 30-inch outside diameter pipeline loop extension, located in Hudspeth County, Texas as part of its Line No. 1110 Loop Project.¹

Submittal of Status Report

In compliance with Section 157.208(c)(10) of the Natural Gas Act, EPNG is providing Environmental Inspector Report for the period of June 10, 2024 through June 16, 2024.

¹ EPNG received a timely protest within 60-days of the date of the notice issued by the Commission. Accordingly, the Project was reviewed as a case-specific certificate application under section 7 of the NGA. On April 25, 2024, the Commission issued an order denying the protest and authorizing EPNG to construct and operate the proposed facilities under its Part 157 blanket certificate.

EPNG's Weekly Environmental Inspection Report No. 5		
Docket No. CP23-546-000		
Project Name:	Line No. 1110 Loop Project	
County/State:	Hudspeth County, Texas	Date: 06/20/2024
Reporting Period:	06/10/2024 – 06/16/2024	
Environmental Inspection:	Chennie Castanon	
<p>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</p> <ul style="list-style-type: none"> • Continued to work on foundations for launcher relocation. • Started welding pipe and x-raying pipe joints. • Started excavations for taps associated with the launcher on EPNG's Line Nos. 1100 and 1103. • Continued to grade along access road and apply water for dust suppression where appropriate. <p>2. RELEVANT ENVIRONMENTAL ACTIVITIES:</p> <p>During this reporting period, the Environmental Inspector (EI) presented the environmental presentation to 19 personnel and supervised the cleanup of a hydraulic fluid leak per the Project's Spill Prevention, Control, and Countermeasure (SPCC) Plan.</p> <p>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN:</p> <p>On 06/10/2024, the contractor's hydrovac truck working at the launcher tap location on EPNG's Line No. 1100 line broke a hydraulic hose and leaked approximately five gallons of hydraulic fluid onto the ground. Work was immediately halted, the leak was contained, and the truck was repaired. All contaminated soil was collected and placed into proper storage containers at the EI's direction. No vegetation or sensitive resources were impacted, and no fluid entered any washes or streams. EPNG is currently coordinating with a lab in El Paso, Texas to test the contaminated soil.</p> <p>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS:</p> <p>No environmental compliance issues or resolutions occurred during this reporting period.</p> <p>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS:</p> <p>No landowner issues or concerns identified during this reporting period.</p> <p>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD:</p> <p>Construction contractor will continue grading activities along the access road, continue welding and x-raying pipe, start ditching and lowering pipe into trench, and complete foundations, fabrication, and welding for relocated launcher.</p>		

Line No. 1110 Loop Project

Location: Immediately southeast of MP 105+00
Direction of Photo: Northeast
Description: Hydrovac activities for the tap associated with the launcher on Line No. 1100.
Date: 06/11/2024




Location: MP 31+00
Direction of Photo: Southwest
Description: Pipe welding.
Date: 06/15/2024



Line No. 1110 Loop Project

Location: MP 105+00
Direction of Photo: Northeast
Description: Pouring concrete for launcher foundation.
Date: 06/15/2024

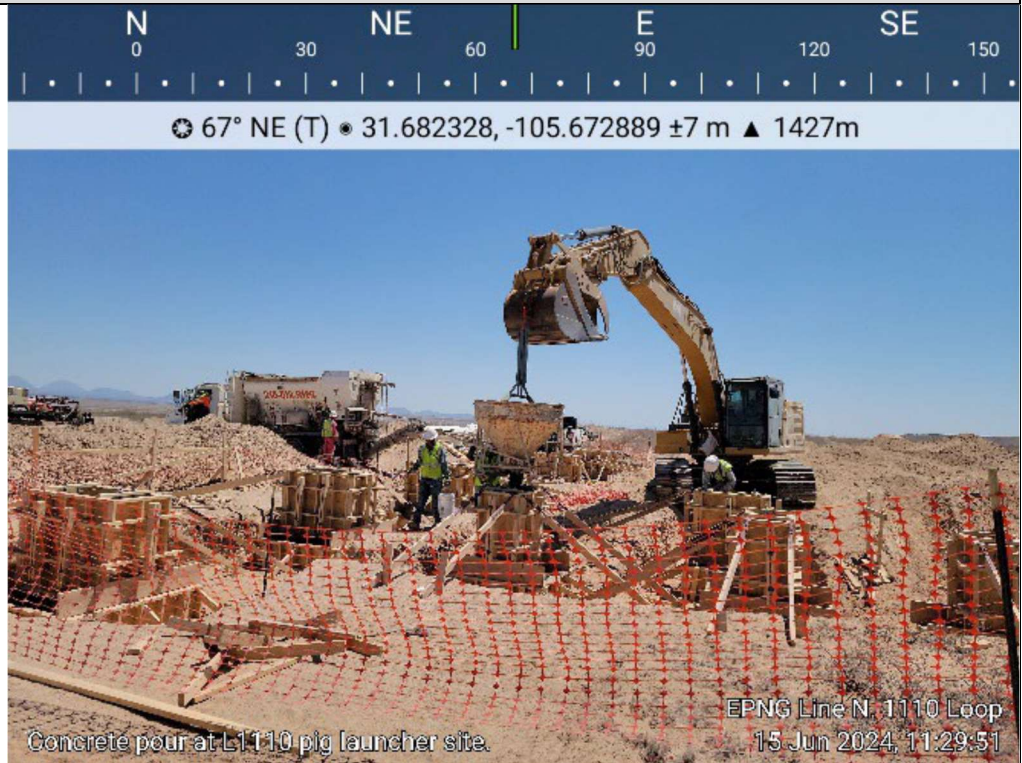

Location: Approximately 108 feet southeast of MP 105+00
Direction of Photo: North
Description: Cleanup activities for hydraulic fluid leak per SPCC Plan.
Date: 06/10/2024

