



May 29, 2024

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne A. Reese, Acting Secretary

Re: El Paso Natural Gas Company, L.L.C.;
Docket No. CP23-546-000
Line No. 1110 Loop Project
Weekly Environmental Inspector Report – May 20, 2024 through May 26, 2024

Commissioners:

El Paso Natural Gas Company, L.L.C. ("EPNG") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP23-546-000, its weekly status report related to the Line No. 1110 Loop Project ("Project").

Description of Proceeding

On September 22, 2023, EPNG submitted a Request for Prior Notice Authorization Pursuant to Blanket Certificate in the above-referenced docket seeking authorization to construct, install, operate and maintain an approximately two-mile 30-inch outside diameter pipeline loop extension, located in Hudspeth County, Texas as part of its Line No. 1110 Loop Project.¹

Submittal of Status Report


In compliance with Section 157.208(c)(10) of the Natural Gas Act, EPNG is providing Environmental Inspector Report for the period of May 20, 2024 through May 26, 2024.

¹ EPNG received a timely protest within 60-days of the date of the notice issued by the Commission. Accordingly, the Project was reviewed as a case-specific certificate application under section 7 of the NGA. On April 25, 2024, the Commission issued an order denying the protest and authorizing EPNG to construct and operate the proposed facilities under its Part 157 blanket certificate.

EPNG's Weekly Environmental Inspection Report No. 2		
Docket No. CP23-546-000		
Project Name:	Line No. 1110 Loop Project	
County/State:	Hudspeth County, Texas	Date: 5/29/2024
Reporting Period:	05/20/2024 – 05/26/2024	
Environmental Inspection:	Chennie Castanon	
<p>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</p> <ul style="list-style-type: none"> • Contractor installed Erosion Control Devices (ECDs), laid mats, and graded along project access road where appropriate. Contractor also began clearing and grading the new right-of-way (ROW) and workspaces. • Contractor excavated Line No. 1110, cut the line, and installed a 30-inch weld cap. Contractor also began activities to decommission/remove the launcher at Valve 19 for relocation. <p>2. RELEVANT ENVIRONMENTAL ACTIVITIES: During this reporting period, the Environmental Inspector (EI) provided environmental training to 28 project personnel, conducted inspection per the Stormwater Pollution Prevention Plan (SWPPP), and inspected all work areas each day for the presence of sensitive species.</p> <p>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN: No environmental problems/issues or corrective actions this reporting period.</p> <p>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS: No environmental compliance issues or resolutions occurred during this reporting period.</p> <p>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS: No landowner issues or concerns identified during this reporting period.</p> <p>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD: Contractor will continue grading activities along the new ROW and workspaces, decommissioning and removing the launcher at Valve 19, and begin skid placement activities.</p>		

Line No. 1110 Loop Project

Location: Access Road at SA001
Direction of Photo: West
Description: Fiber roll erosion control device.
Date: 05/23/2024

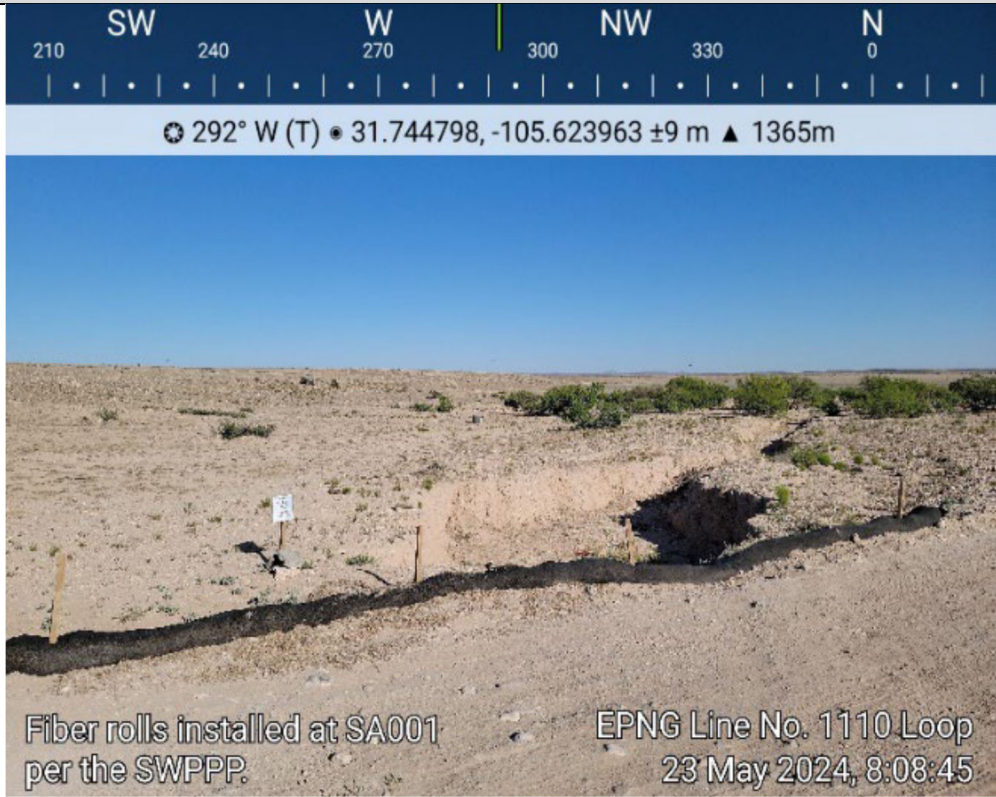

Location: Pipeline ROW
Direction of Photo: East
Description: Clearing vegetation along workspaces and new ROW.
Date: 05/24/2024



Line No. 1110 Loop Project

Location: MP 0+00
Direction of Photo: East
Description: Excavation of Line No. 1110.
Date: 05/24/2024



Location: MP 0+00
Direction of Photo: East
Description: Preparing Line No. 1110 for weld cap.
Date: 05/24/2024

