

November 15, 2024

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne Reese, Secretary

Re: Wyoming Interstate Company, L.L.C.;
Docket No. CP24-20-000,
Cheyenne to Piceance Expansion Capacity Project
Weekly Environmental Inspector Report No. 12

Commissioners:

Wyoming Interstate Company, L.L.C. (“WIC”) is hereby filing with the Federal Energy Regulatory Commission (“Commission”) in Docket No. CP24-20-000, its weekly status report related to WIC’s Cheyenne to Piceance Expansion Capacity Project (“Project”).

Description of Proceeding

On November 29, 2023, WIC filed a prior notice request pursuant to Sections 157.205, 157.208 and 157.210 of the Commission’s regulations under the Natural Gas Act, and WIC’s blanket certificate issued in Docket No. CP83-22-000, for authorization to make certain modifications at its existing Wamsutter Compressor Station in Sweetwater County, Wyoming in order to generate incremental east to west firm natural gas transportation capacity of approximately 180,000 dekatherms per day on WIC’s mainline system.¹

Submittal of Status Report

In compliance with Section 157.208(c)(10) of the Natural Gas Act, WIC is providing Environmental Inspector Report No. 12.

Filing Information

WIC is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

¹ On December 6, 2023, the Commission issued a Notice of Request Under Blanket Authorization initiating the 60-day comment period to allow for any person or Commission’s staff to file motions or notice to intervene and protests. Since no protests were filed within the comment period, the Project was deemed to be authorized on February 5, 2024.

Respectfully submitted,
WYOMING INTERSTATE COMPANY,
L.L.C.

By _____ /s/
Francisco Tarin
Director, Regulatory


Enclosures

Cc. Joel Cornwall, OEP

Wyoming Interstate Company, L.L.C. (WIC)		
WIC's Weekly Environmental Inspection Report No. 12		
Docket No. CP24-20-000		
Project Name:	Cheyenne to Piceance Expansion Capacity Project	
County/State:	Sweetwater County, Wyoming	Date: 11/15/2024
Reporting Period:	November 3, 2024 through November 9, 2024	
Environmental Inspector:	Micah Hill	
<p>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD: During this reporting period, crews poured concrete for the auxiliary building foundation walls and for the cooler footers. Blankets and heaters were then placed over the poured walls due to cold weather. Near the end of the week, crews removed heaters and forms from the auxiliary building walls and began to backfill and perform compaction activities.</p> <p>2. RELEVANT ENVIRONMENTAL ACTIVITIES: During this reporting period, the Environmental Inspector (EI) and WIC personnel provided environmental training to five (5) project personnel.</p> <p>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN: Approximately 2.2 gallons of diesel fuel accidentally spilled as a result of a punctured fuel tank on a hydrovac truck on November 8, 2024. The spill was contained, the vehicle was removed from the site, and contaminated soil was collected for disposal. No waterbodies or sensitive resources were affected. The amount of diesel that was spilled did not trigger any additional reporting requirements.</p> <p>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS: No environmental compliance issues or resolutions occurred during this reporting period.</p> <p>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS: No landowner issues or concerns identified during this reporting period.</p> <p>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD: Work planned for the next reporting period includes: (i) the removal of pipe valves and fittings from the turbine compressor unit within the existing compressor building, (ii) removal of the filter separator system, (iii) work on the coalescing filter foundation, (iv) completion of grading activities, and (v) pour the floor for the auxiliary building.</p>		


Cheyenne to Piceance Expansion Capacity Project Photo Documentation


Location: Wamsutter Compressor Station
Direction of Photo: Southeast
Description: Soil compaction of the auxiliary building foundations.
Date: 11/05/2024

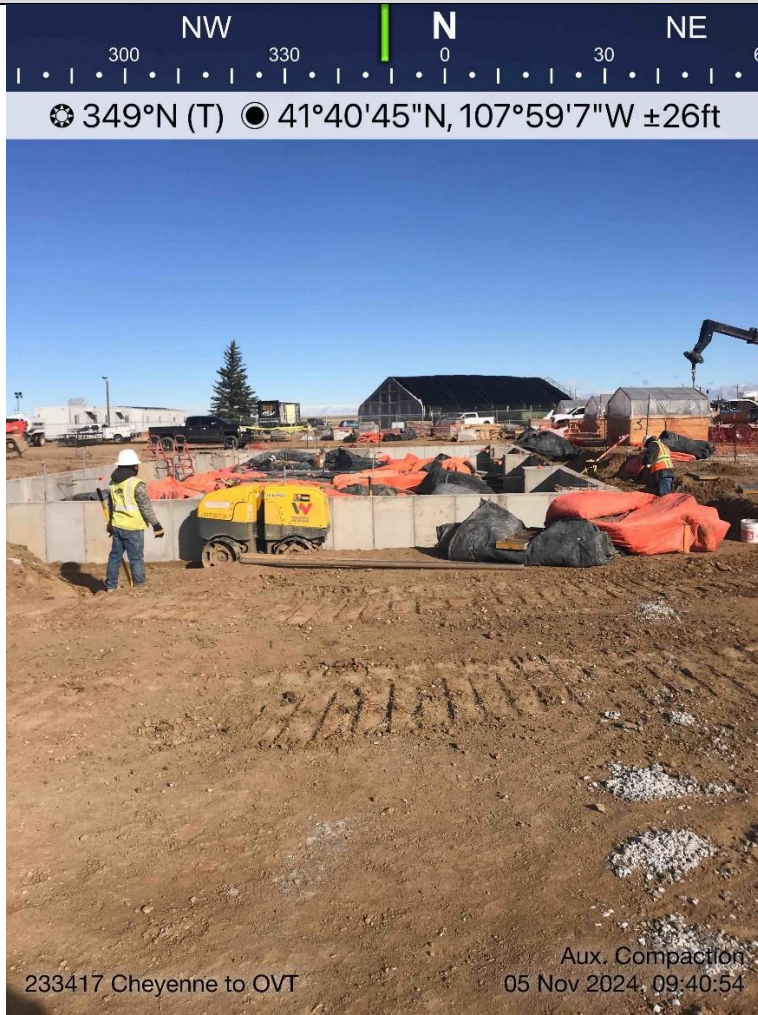


Location: Wamsutter
Compressor Station
Direction of Photo:
Southeast
Description: Freeze
blankets on the cooler
footers.
Date: 11/7/2024



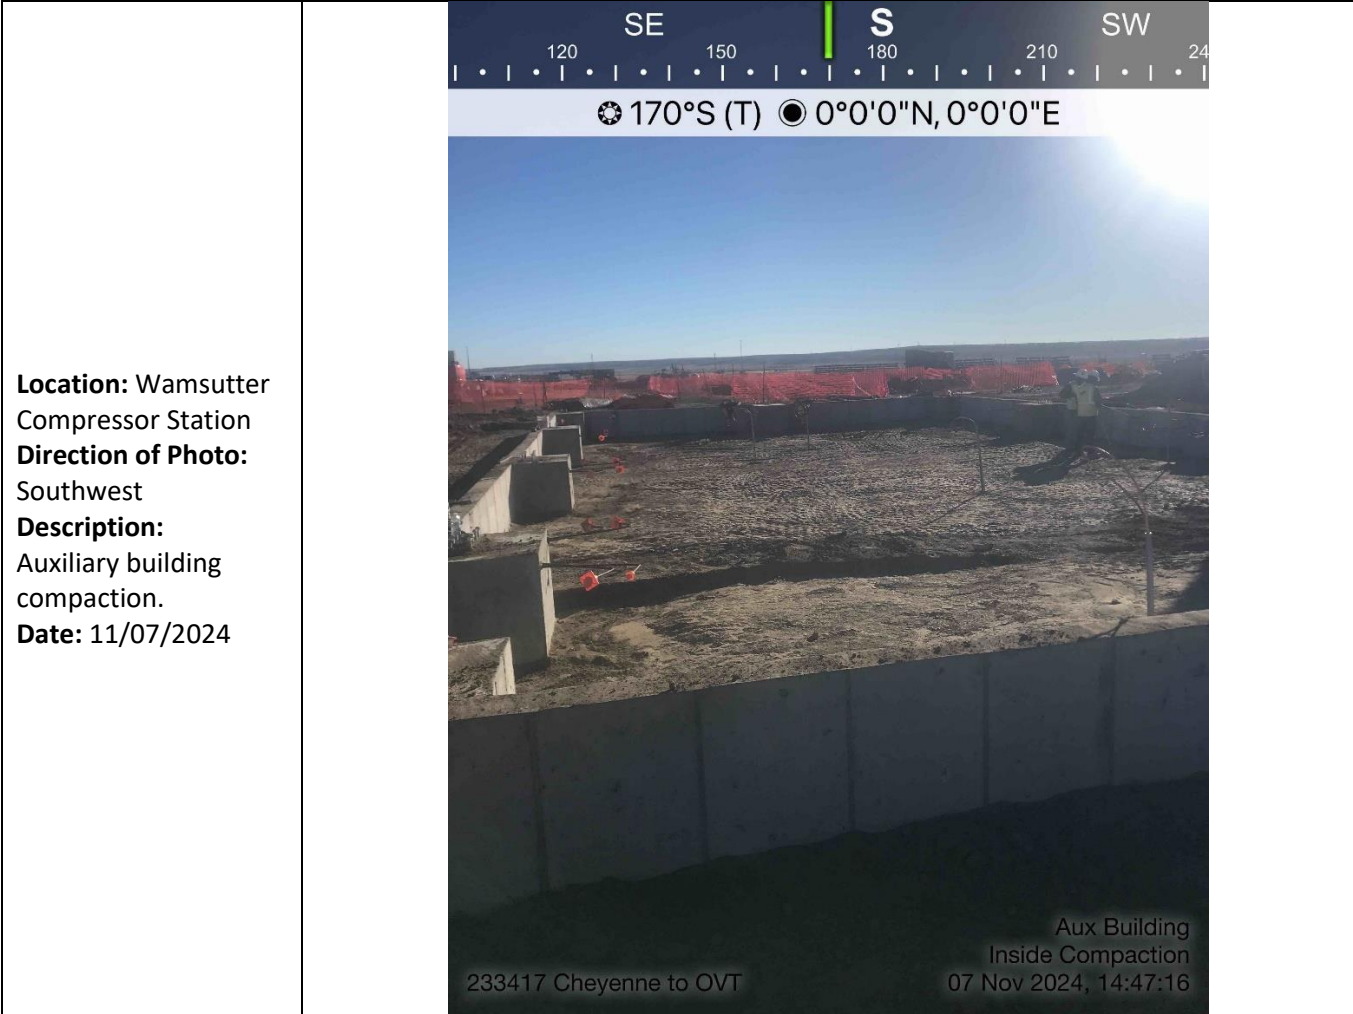

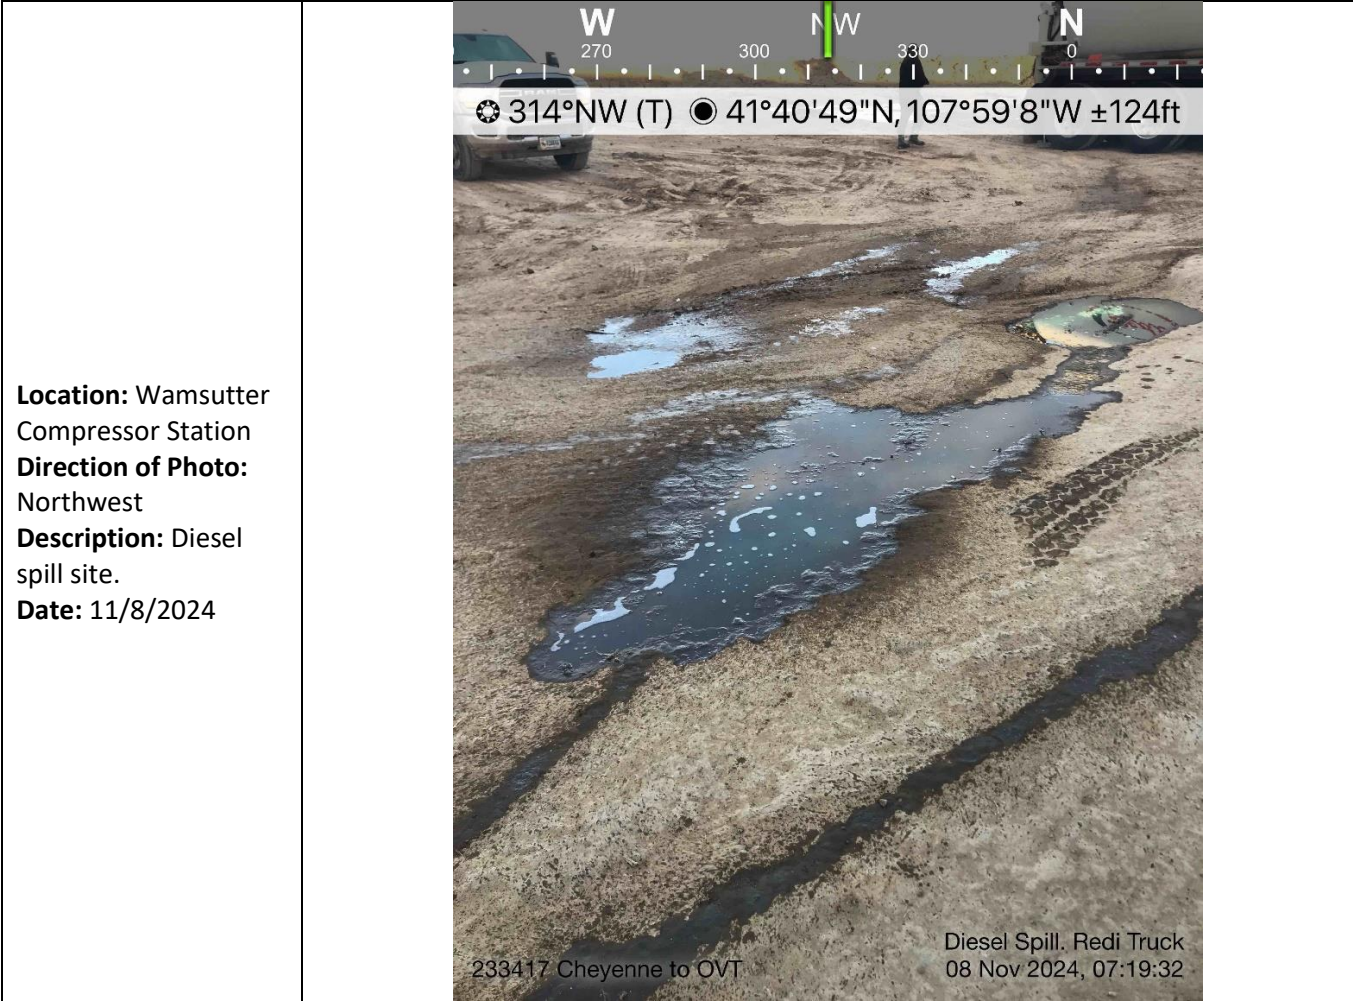

<p>Location: Wamsutter Compressor Station Direction of Photo: Northwest Description: Diesel spill site after cleanup. Date: 11/8/2024</p>	
-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------	-------------------------------------------------------------------------------------

