

June 26, 2025

Federal Energy Regulatory Commission  
888 First Street, N.E.  
Washington, D.C. 20426

Attention: Ms. Debbie-Anne Reese, Secretary

Re: Wyoming Interstate Company, L.L.C.;  
Docket No. CP24-20-000,  
Cheyenne to Piceance Expansion Capacity Project  
Weekly Environmental Inspector Report No. 44

Commissioners:

Wyoming Interstate Company, L.L.C. ("WIC") is hereby filing with the Federal Energy Regulatory Commission ("Commission") in Docket No. CP24-20-000, its weekly status report related to WIC's Cheyenne to Piceance Expansion Capacity Project ("Project").

### **Description of Proceeding**

On November 29, 2023, WIC filed a prior notice request pursuant to Sections 157.205, 157.208 and 157.210 of the Commission's regulations under the Natural Gas Act, and WIC's blanket certificate issued in Docket No. CP83-22-000, for authorization to make certain modifications at its existing Wamsutter Compressor Station in Sweetwater County, Wyoming in order to generate incremental east to west firm natural gas transportation capacity of approximately 180,000 dekatherms per day on WIC's mainline system.<sup>1</sup>

### **Submittal of Status Report**

In compliance with Section 157.208(c)(10) of the Natural Gas Act, WIC is providing Environmental Inspector Report No. 44.

### **Filing Information**

WIC is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

---

<sup>1</sup> On December 6, 2023, the Commission issued a Notice of Request Under Blanket Authorization initiating the 60-day comment period to allow for any person or Commission's staff to file motions or notice to intervene and protests. Since no protests were filed within the comment period, the Project was deemed to be authorized on February 5, 2024.



# Wyoming Interstate Company, L.L.C.

<b>Wyoming Interstate Company, L.L.C. (WIC)</b>		
<b>WIC's Weekly Environmental Inspection Report No. 44</b>		
<b>Docket No. CP24-20-000</b>		
<b>Project Name:</b>	<b>Cheyenne to Piceance Expansion Capacity Project</b>	
<b>County/State:</b>	Sweetwater County, Wyoming	<b>Date:</b> 6/26/2025
<b>Reporting Period:</b>	June 15, 2025 through June 21, 2025	
<b>Environmental Inspector:</b>	Micah Hill	
<p><b>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD:</b>  During this reporting period, crews: (i) completed the installation of pipe supports at the cooler risers, (ii) began underground coating and above grade painting of lines, (iii) completed various tie-ins and set compressors for the air movers in preparation for the outage, (iv) continued installing stainless steel tubing to instruments and valves, and (v) used a water truck to control dust.</p> <p><b>2. RELEVANT ENVIRONMENTAL ACTIVITIES:</b>  During this reporting period, the Environmental Inspector (EI) and WIC personnel did not provide environmental training to any project personnel.</p> <p><b>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN:</b>  No environmental problems or issues occurred during this reporting period.</p> <p><b>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS:</b>  No environmental compliance issues or resolutions occurred during this reporting period.</p> <p><b>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS:</b>  No landowner issues or concerns identified during this reporting period.</p> <p><b>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD:</b>  Work planned for the next reporting period includes: (i) completion of the second outage, (ii) start commissioning of the station, (iii) continued backfill activities, and (iv) completion of hydrostatic tests 8 and 9.</p>		

Cheyenne to Piceance Expansion Capacity Project Photo Documentation

**Location:** Wamsutter Compressor Station  
**Direction of Photo:** Southwest  
**Description:** Air mover installed.  
**Date:** 6/17/2025




**Location:** Wamsutter Compressor Station  
**Direction of Photo:** Southeast  
**Description:** Excavation of tie-in point on 30-inch pipeline.  
**Date:** 6/18/2025



**Location:** Wamsutter  
Compressor Station  
**Direction of Photo:**  
Northeast  
**Description:** Completed  
sleeper form under new  
piping  
**Date:** 6/21/2025



**Location:** Wamsutter  
Compressor Station  
**Direction of Photo:**  
South  
**Description:** Tie-in  
piping installed.  
**Date:** 6/21/2025

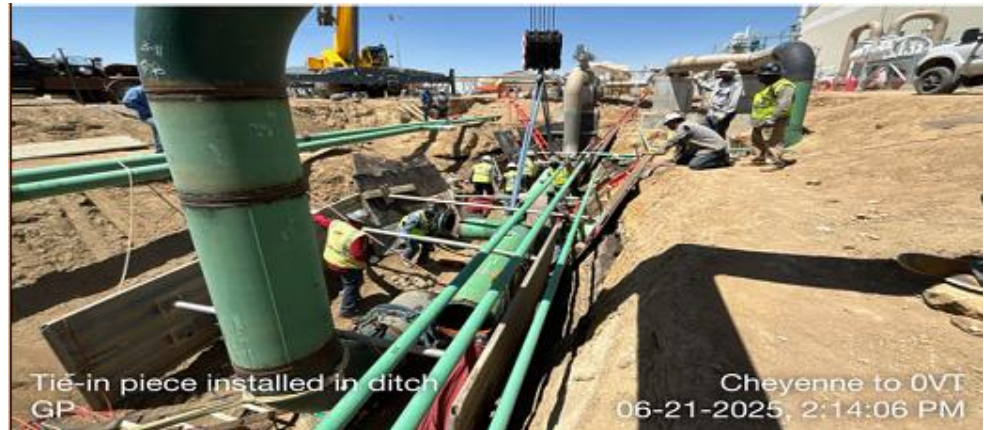

**Certificate of Service**

I hereby certify that I have this day caused a copy of the foregoing documents to be served upon each person designated on the official service list compiled by the Commission's Secretary in this proceeding in accordance with the requirements of Section 385.2010 of the Federal Energy Regulatory Commission's Rules of Practice and Procedure.

Dated at Colorado Springs, Colorado as of this 26<sup>th</sup> day of June 2025.

\_\_\_\_\_  
/s/

Francisco Tarin

Two North Nevada Avenue  
Colorado Springs, Colorado 80903  
(719) 667-7517
