

December 23, 2024

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne Reese, Secretary

Re: Wyoming Interstate Company, L.L.C.;
Docket No. CP24-20-000,
Cheyenne to Piceance Expansion Capacity Project
Weekly Environmental Inspector Report No. 18

Commissioners:

Wyoming Interstate Company, L.L.C. (“WIC”) is hereby filing with the Federal Energy Regulatory Commission (“Commission”) in Docket No. CP24-20-000, its weekly status report related to WIC’s Cheyenne to Piceance Expansion Capacity Project (“Project”).

Description of Proceeding

On November 29, 2023, WIC filed a prior notice request pursuant to Sections 157.205, 157.208 and 157.210 of the Commission’s regulations under the Natural Gas Act, and WIC’s blanket certificate issued in Docket No. CP83-22-000, for authorization to make certain modifications at its existing Wamsutter Compressor Station in Sweetwater County, Wyoming in order to generate incremental east to west firm natural gas transportation capacity of approximately 180,000 dekatherms per day on WIC’s mainline system.¹

Submittal of Status Report

In compliance with Section 157.208(c)(10) of the Natural Gas Act, WIC is providing Environmental Inspector Report No. 18.

Filing Information

WIC is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

¹ On December 6, 2023, the Commission issued a Notice of Request Under Blanket Authorization initiating the 60-day comment period to allow for any person or Commission’s staff to file motions or notice to intervene and protests. Since no protests were filed within the comment period, the Project was deemed to be authorized on February 5, 2024.

Respectfully submitted,
WYOMING INTERSTATE COMPANY,
L.L.C.

By _____ /s/
Francisco Tarin
Director, Regulatory

Enclosures

Cc. Joel Cornwall, OEP

Wyoming Interstate Company, L.L.C.

Wyoming Interstate Company, L.L.C. (WIC)		
Weekly Environmental Inspection Report No. 18		
Docket No. CP24-20-000		
Project Name:	Cheyenne to Piceance Expansion Capacity Project	
County/State:	Sweetwater County, Wyoming	Date: 12/23/2024
Reporting Period:	December 15, 2024 through December 21, 2024	
Environmental Inspector:	Micah Hill	
1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD: During this reporting period, crews: (i) finished building and installing forms then poured concrete for the pipe support foundations and the cable tray supports, (ii) completed the structural steel installation and hung sheet metal on the west side of the auxiliary building, (iii) excavated the blowdown silencer foundation, (iv) continued fabrication and painting activities, and (v) inspected the site for environmental issues in preparation of the upcoming holiday.		
2. RELEVANT ENVIRONMENTAL ACTIVITIES: During this reporting period, the Environmental Inspector (EI) and WIC personnel provided environmental training to one (1) project personnel.		
3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN: No environmental problems/issues or corrective actions this reporting period.		
4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS: No environmental compliance issues or resolutions occurred during this reporting period.		
5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS: No landowner issues or concerns identified during this reporting period.		
6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD: No construction activities are planned for the next reporting period due to the Christmas holiday. WIC operation personnel will be on site throughout the holiday to address any environmental issues.		



Cheyenne to Piceance Expansion Capacity Project Photo Documentation

Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Auxiliary building structural steel installed.
Date: 12/16/2024



Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Compaction activities for the forms at the cable tray supports.
Date: 12/16/2024



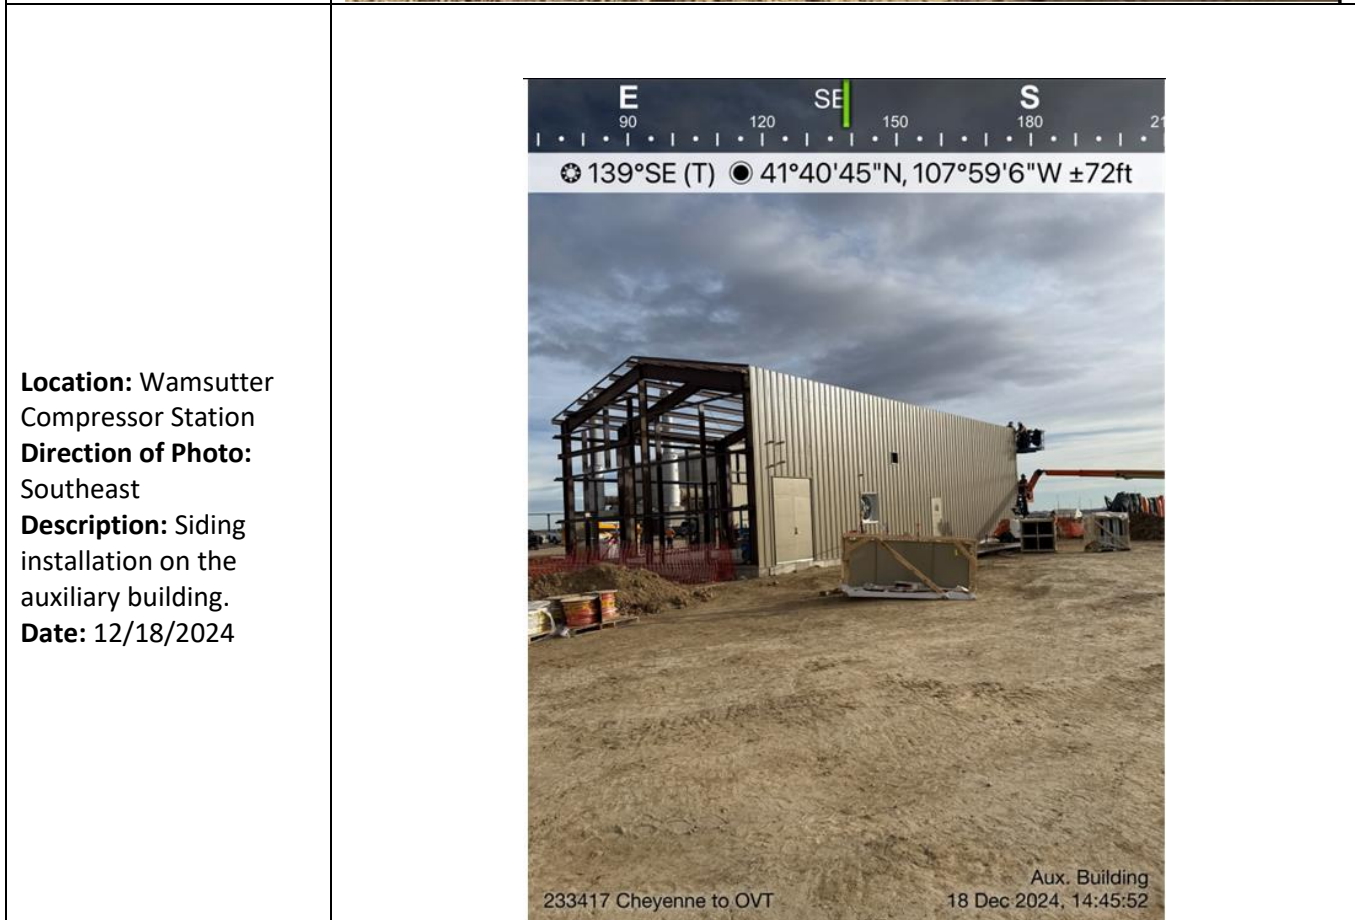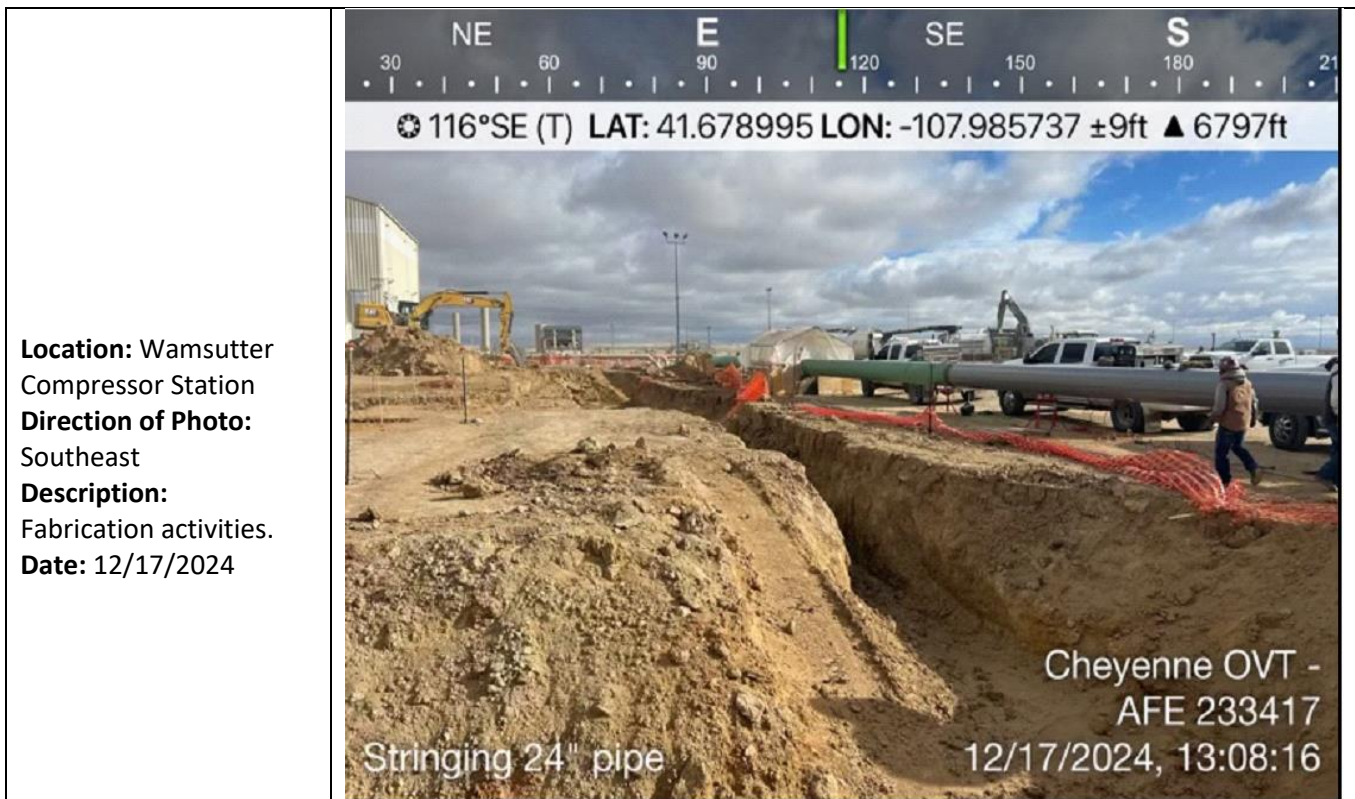

Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Cable tray footers completed.
Date: 12/20/2024



Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Blow down silencer foundation excavated.
Date: 12/20/2024



