



March 20, 2025

Federal Energy Regulatory Commission
888 First Street, N.E.
Washington, D.C. 20426

Attention: Ms. Debbie-Anne Reese, Secretary

Re: Wyoming Interstate Company, L.L.C.;
Docket No. CP24-20-000,
Cheyenne to Piceance Expansion Capacity Project
Weekly Environmental Inspector Report No. 30

Commissioners:

Wyoming Interstate Company, L.L.C. (“WIC”) is hereby filing with the Federal Energy Regulatory Commission (“Commission”) in Docket No. CP24-20-000, its weekly status report related to WIC’s Cheyenne to Piceance Expansion Capacity Project (“Project”).

Description of Proceeding

On November 29, 2023, WIC filed a prior notice request pursuant to Sections 157.205, 157.208 and 157.210 of the Commission’s regulations under the Natural Gas Act, and WIC’s blanket certificate issued in Docket No. CP83-22-000, for authorization to make certain modifications at its existing Wamsutter Compressor Station in Sweetwater County, Wyoming in order to generate incremental east to west firm natural gas transportation capacity of approximately 180,000 dekatherms per day on WIC’s mainline system.¹

Submittal of Status Report

In compliance with Section 157.208(c)(10) of the Natural Gas Act, WIC is providing Environmental Inspector Report No. 30.

Filing Information

WIC is e-Filing this letter and report with the Commission's Secretary in accordance with the Commission's Order No. 703, *Filing Via the Internet*, guidelines issued on November 15, 2007 in Docket No. RM07-16-000.

¹ On December 6, 2023, the Commission issued a Notice of Request Under Blanket Authorization initiating the 60-day comment period to allow for any person or Commission’s staff to file motions or notice to intervene and protests. Since no protests were filed within the comment period, the Project was deemed to be authorized on February 5, 2024.

Respectfully submitted,
WYOMING INTERSTATE COMPANY,
L.L.C.

By _____ /s/
Francisco Tarin
Director, Regulatory

Enclosures


Cc. Joel Cornwall, OEP

Wyoming Interstate Company, L.L.C.

Wyoming Interstate Company, L.L.C. (WIC)		
WIC's Weekly Environmental Inspection Report No. 30		
Docket No. CP24-20-000		
Project Name:	Cheyenne to Piceance Expansion Capacity Project	
County/State:	Sweetwater County, Wyoming	Date: 3/20/2025
Reporting Period:	March 9, 2025 through March 15, 2025	
Environmental Inspector:	Micah Hill	
<p>1. SUMMARY OF CONSTRUCTION ACTIVITY FOR INSPECTION PERIOD: During this reporting period crews: (i) poured pipe supports for the wastewater tank, (ii) continued running conduit to new valve locations behind the compressor building, (iii) poured red-dyed cement on the ducts in order to identify them, (iv) continued installing the station recycle valve piping, (v) continued installing the recycle and gas vent lines, (vi) backfilled the 2-inch drain vent, fuel gas, utility air and instrument air lines north of the compressor building, and (vii) excavated a 2-inch emergency shutdown slot trench.</p> <p>2. RELEVANT ENVIRONMENTAL ACTIVITIES: During this reporting period, the Environmental Inspector (EI) and WIC personnel provided environmental training to one (1) project personnel.</p> <p>3. ENVIRONMENTAL PROBLEMS/ISSUES AND CORRECTIVE ACTIONS TAKEN: No environmental problems/issues or corrective actions this reporting period.</p> <p>4. ENVIRONMENTAL COMPLIANCE ISSUES/RESOLUTIONS: No environmental compliance issues or resolutions occurred during this reporting period.</p> <p>5. ISSUES AND CONCERNS IDENTIFIED BY LANDOWNERS: No landowner issues or concerns identified during this reporting period.</p> <p>6. WORK PLANNED FOR THE FOLLOWING REPORTING PERIOD: Work planned for the next reporting period includes: (i) completing the high-pressure gas piping installation, (ii) installation of the actuator valves, (iii) completion of the fourth hydrotest section, and (iv) installation of the 20-inch recycle, 6-inch gas vent, and emergency shut down lines.</p>		

Cheyenne to Piceance Expansion Capacity Project Photo Documentation

Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Pouring pipe supports for the wastewater tank.
Date: 3/10/2025

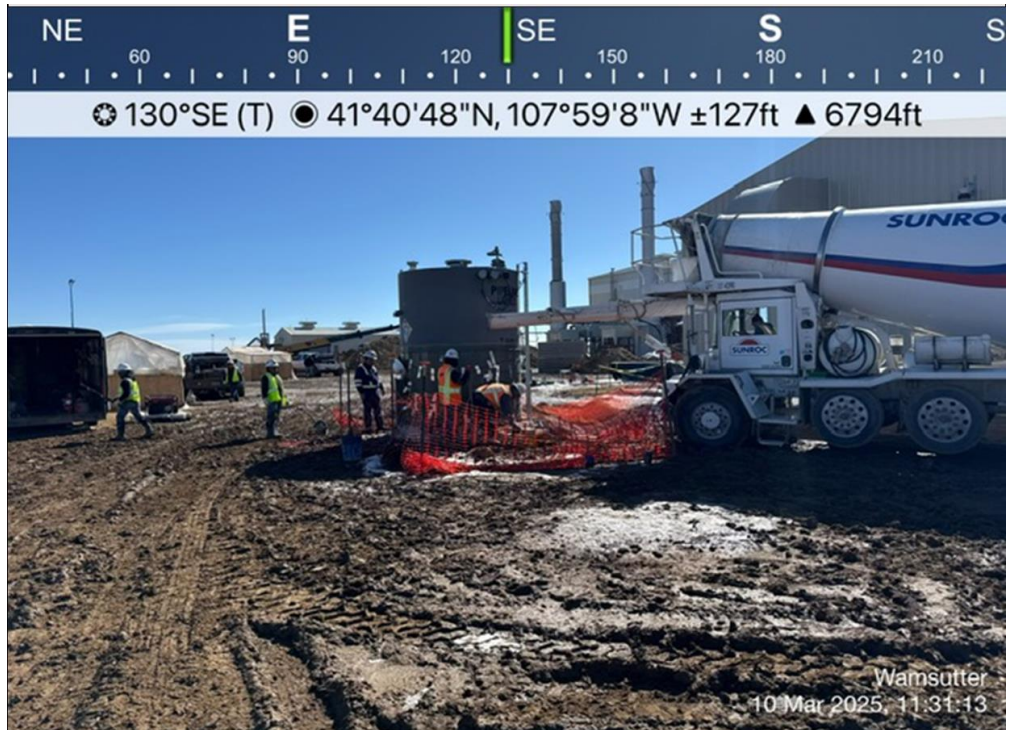

Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Installing the 20-inch recycle line.
Date: 3/11/2025



Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Installing ducts behind the compressor building.
Date: 3/11/2025



Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Installing 3-inch gas vent lines.
Date: 3/12/2025



Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Installing 2-inch emergency shut down lines.
Date: 3/13/2025



Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Pouring red cement on the ducts.
Date: 3/14/2025



Location: Wamsutter Compressor Station
Direction of Photo: N/A
Description: Hydrovac excavation for emergency shutdown line slot trenches
Date: 3/14/2025



